




CLIENT 	CONSULTANT 	CONTRACTOR 
Date: 23-Dec-25		Ref. No. : CCECC-R1181-2-CC-DS-013 Rev. No.: 00
DOCUMENT SUBMITTAL		
PROJECT: R1181/2 Improvement of Al Safa Road		
We hereby submit the following for your approval/records: Subject : Project Emergency Preparedness and Response Plan (PEPRP)		
Attached Documents: RECEIVED 14 DEC 2025 7:40 am PARSONS R1181-2		
Other Remarks:		
		
Approval Required by: For CONTRACTOR 	MOHSEN D. GAZZAZ - PROJECT DIRECTOR - SIGNATURE: 	
Remarks : Comments Attached		
Engineer's Reply: ☐ Approved ☒ Approved as Noted ☐ Revise & Re-submit ☐ Rejected 		
For the ENGINEER	PROJECT DIRECTOR	Signature:  Date:

CCECC
 Dubai, UAE
 Project: RTA (R1181-2)
 06 JAN 2026
RECEIVED
 BY:  Time: 7:45 am

DISTRIBUTION		FILE NO:		
CCECC				
PROJECT: RTA (R1181/2) - IMPROVEMENT OF AL BAFA STREET				
DOCUMENT / CORRESPONDENCE DISTRIBUTION				
TO	INITIALS	ACTION	REVIEW	INFO
O.B				
B.D.D				
PB/PM				
BPM				
PLANNING				
COMMERCIAL / QS				
HSE				
TRAFFIC				
DESIGN / TECHNICAL				
QA/QC / MATERIAL				
NOC				
CONSTRUCTION BRIDGE				
CONSTRUCTION ROAD				
CONSTRUCTION UTILITY				
SURVEYOR				
STORE				
HEAD OFFICE				
SUBC ON				
OTHERS				

[Signature]
6/1/26

CLIENT 	CONSULTANT 	CONTRACTOR 
Date: 23-Dec-25		Ref. No. : CCECC-R1181-2-CC-DS-013 Rev. No.: 00
DOCUMENT SUBMITTAL		
PROJECT: R1181/2 Improvement of Al Safa Road		
We hereby submit the following for your approval/records: Subject : Project Emergency Preparedness and Response Plan (PEPRP)		
Attached Documents:		
Other Remarks:		
		
Approval Required by:		
For CONTRACTOR: 	MOHSEN D. GAZZAZ - PROJECT DIRECTOR - SIGNATURE: 	
Remarks :	Comments:	
Engineer's Reply:		
☐ Approved ☒ Approved as Noted ☐ Revise & Re-submit ☐ Rejected 1. This is live document can be reviewed and modified as necessary. 2. Emergency Mock up drill shall be conducted as per schedule 3. The emergency Contact number shall be displayed on work location. 4. Emergency preparedness resources shall be checked regularly. 		
For the ENGINEER PROJECT DIRECTOR Signature: Date:		



PROJECT EMERGENCY PREPAREDNESS AND RESPONSE PLAN (PEPRP)

ABSTRACT

This Emergency Preparedness and Response Plan (EPRP) for Project R1181/2 – Improvement of Al Safa Road provides a PDCA-based framework for managing foreseeable emergencies throughout the project lifecycle. Fully compliant with RTA MSTG C.9, UAE regulations, and ISO 45001 / ISO 22301, the plan prioritises life safety, public protection, environmental safeguarding, and rapid recovery through defined roles, resources, training, drills, and coordination with external authorities.

Document Reference No.: CCECC-R1181/2-PEPRP-PLN-07

Document Control

PROJECT EMERGENCY PREPAREDNESS AND RESPONSE PLAN (PEPRP)

PROJECT NO. R1181/2.

PROJECT NAME. IMPROVEMENT OF AL WASL,
JUMEIRAH, AL SAFA, AND UMM
SUQEIM ROADS

IMPROVEMENT OF AL SAFA
STREET

Client



Roads & Transport Authority Roads
Department.
P.O. Box 118899
Dubai – U.A.E.

Consultant



Parsons Overseas Limited.
Oud Metha Road.
PO Box 9123
Dubai – U.A.E.

Contractor




CCECC Dubai Branch – DIP 1
European Business Centre, Level 3,
354, P.O. Box 394329,
Dubai – U.A.E.

This Version-00


Authored by:

Name: SHAHID AHMAD
Role: Safety Engineer
Signed: 
Date: 23/12/2025


Reviewed by:

Name: MIRZA SHAHABUDDIN BAIG
Role: Project HSE Manager
Signed: 
Date: 23-12-25

Reviewed by:

Name: AHMED ELKADI / GUO PENGCHENG
Role: Deputy Project Manager
Signed: 
Date: 23/12/2025

Authorised for issue by:

Name: MOHSEN D GAZZAZ
Role: Project Director
Signed: 
Date: 23/12/2025

Version History - To Consultant

Rev. No.	Date	Status and Purpose	Prepared By	Changes Overview	Reviewed By	Approved By
00 (Draft)	09-Dec-25	Initial draft for internal review	HSE Engineer	N/A	HSEM / DPM	PD
00	23-Dec-25	For Approval	HSE Engineer	Final for approval	HSEM / DPM	PD

Contents

SECTION 1 – GENERAL	5
1.1 INTRODUCTION – PDCA BASED APPROCH.....	5
1.2 SCOPE OF THE EPRP.....	5
1.3 APPROVAL OF THE PROJECT EMERGENCY PREPAREDNESS AND RESPONSE PLAN	6
1.4 DOCUMENT CONTROL AND VERSION MANAGEMENT	6
1.5 ABBREVIATIONS AND DEFINITIONS	6
1.5.1 ABBREVIATIONS.....	6
1.5.2 DEFINITIONS (KEY TERM)	7
1.6 REFERENCE DOCUMENTS AND STANDARDS.....	7
SECTION 2 – PROJECT DETAILS	8
2.1 PROJECT SCOPE OF WORK (EMERGENCY RELATED).....	8
2.2 PROJECT OVERVIEW	8
2.3 FORESEEABLE EMERGENCIES – PROJECT RISK CONTEXT	8
2.4 EPRP OBJECTIVES.....	9
2.5 PROJECT IDENTIFICATION.....	9
2.6 PROJECT KEY PERSONNEL AND EMERGENCY CONTACT NUMBERS.....	10
2.7 SITE CONSTRAINTS AFFECTING EMERGENCY RESPONSE	11
SECTION 3 – INTRODUCTION, PURPOSE, SCOPE & COMMITMENT OF EPRP	12
3.1 PURPOSE OF THE EPRP.....	12
3.2 SCOPE OF THE PLAN	12
3.3 MANAGEMENT COMMITMENT & PDCA APPLICATION.....	12
SECTION 4 –EMERGENCY RESPONSE PLANING (PLAN PHASE- PDCA)	13
4.1 PLANNING OBJECTIVES	13
4.2 EMERGENCY HAZARD IDENTIFICATION, PRIORITY & ALARP CONTROLS.....	14
4.3 FORESEEABLE EMERGENCY SCENARIOS SUMMARY.....	15
4.4 EMERGENCY SCENARIO–WISE PLANNED RESPONSE STRATEGY (PLAN PHASE).....	16
4.5 ROLES & RESPONSIBILITIES – EMERGENCY PLANNING DUTIES (PLAN PHASE)	17
4.6 EMERGENCY RESOURCES & EQUIPMENT PLANNING	18
4.7 EMERGENCY COMMUNICATION, ESCALATION & ACCESS ROUTE PLANNING	19
4.7 A – EMERGENCY COMMUNICATION & ESCALATION PLAN	19
4.7 B – EMERGENCY ESCALATION LEVELS	19
4.8 EMERGENCY ROUT PLANNING (VEHICLE ACCESS & ASSEMBLY ACCESS)	20
4.8 A – EMERGENCY VEHICLE ACCESS & EXIT ROUTES.....	20
4.8 B EMERGENCY ASSEMBLY POINTS & SITE LAYOUT.....	20
4.9 EMERGENCY TRAINING & COMPETENCY PLANNING (PLAN PHASE – PDCA).....	21
4.9 A – EMERGENCY TRAINING NEEDS ANALYSIS & PLANNING MATRIX.....	21
4.9B – EMERGENCY TRAINING FREQUENCY & COMPETENCY VALIDATION.....	22
4.9 C – EMERGENCY TRAINING PLANNING CONTROL	23
4.10 EMERGENCY DRILL PLANNING (LINK TO DO & CHECK PHASES).....	23
SECTION 5 – EMERGENCY PREPAREDNESS IMPLEMENTATION (DO PHASE)	26
5.1 IMPLEMENTATION OF OBJECTIVES	26
5.2 IMPLEMENTATION OF EMERGENCY RESPONSE PROCEDURES (ERPs).....	27
5.3 ERP IMPLEMENTATION (EXECUTION) STEPS (COMMON FOR ALL)	28
5.4 EMERGENCY DRILL EXECUTION.....	29
5.5 COORDINATION WITH EXTERNAL AGENCIES	29
5.6 RECORDS & MONITORING.....	29
5.7 PERFORMANCE MONITORING INDICATORS	30
5.8 CORRECTIVE ACTIONS.....	30
SECTION 6 – MONITORING, MEASUREMENT, AUDIT & REVIEW (CHECK PHASE – PDCA)	31

6.1 EMERGENCY PERFORMANCE MONITORING FRAMEWORK.....	31
6.2 EMERGENCY DRILL EVALUATION & REVIEW.....	31
6.3 INCIDENT & NEAR-MISS REVIEW	32
6.4 EMERGENCY KPI MONITORING.....	32
6.5 EMERGENCY EQUIPMENT INSPECTION & VERIFICATION.....	32
6.6 TRAINING & COMPETENCY VERIFICATION	33
6.7 COMMUNICATION & ESCALATION REVIEW.....	33
6.8 INTERNAL AUDIT & COMPLIANCE REVIEW.....	33
6.9 INTERNAL AUDIT & COMPLIANCE REVIEW.....	34
6.10 OUTPUTS TO ACT PHASE.....	34
SECTION 7 – ACT - CORRECTIVE ACTION & CONTINUAL IMPROVEMENT.....	35
7.1 INPUTS TO THE ACT PHASE.....	35
7.2 CORRECTIVE ACTION MANAGEMENT.....	35
7.3 PREVENTIVE ACTION MANAGEMENT	36
7.4 UPDATE & REVISION OF EMERGENCY DOCUMENTS	36
7.5 MANAGEMENT REVIEW & DECISION MAKING	36
7.6 CONTINUAL IMPROVEMENT MECHANISM.....	37
7.7 COMMUNICATION OF LESSONS LEARNED	37
7.8 VERIFICATION OF ACT PHASE EFFECTIVENESS.....	37
7.9 PDCA CYCLE CLOSURE.....	38
SECTION 8 – EMERGENCY RESPONSE PROCEDURES	39
8.1 FIRE & EXPLOSION (ERP-P01).....	40
8.2 EXCAVATION & TEMPORARY WORKS COLLAPSE RESPONSE PROCEDURE (ERP-P02)	43
8.3 FALL FROM HEIGHT & SUSPENSION TRAUMA RESPONSE PROCEDURE (ERP-P03)	46
8.4 UTILITY STRIKE RESPONSE PROCEDURE (ERP-P04).....	49
8.5 TRAFFIC INCIDENT & PUBLIC SAFETY RESPONSE PROCEDURE (ERP-P05)	53
8.6 MEDICAL EMERGENCY & HEAT STRESS RESPONSE PROCEDURE (ERP-P06)	58
8.7 ENVIRONMENTAL SPILL RESPONSE PROCEDURE (ERP-P07)	62
8.8 ERP-P08 – EXTREME WEATHER RESPONSE PROCEDURE (FLOOD / SANDSTORM).....	66
8.9 ERP- CONFINED SPACE RESCUE RESPONSE PROCEDURE	70
8.10 ERP- MOBILE / CRAWLER CRANE EMERGENCY & RESCUE PROCEDURE	73
8.11 ERP- P11 - PANDEMIC / INFECTIOUS DISEASE RESPONSE PROCEDURE	76
SECTION 09 – ANNEXURES.....	79
10.1 ANNEXURE A – EMERGENCY CONTACT LIST	79
10.2 ANNEXURE B – OFFICE EMERGENCY EVACUATION LAYOUT PLAN	79
10.3 ANNEXURE C – NEAREST HOSPITAL LOCATION LAYOUT PLAN.....	79
10.4 ANNEXURE D – EMERGENCY DRILL REPORT FORM	79
10.5 ANNEXURE E – INCIDENT / ACCIDENT REPORT FORM.....	79
10.6 ANNEXURE F – EMERGENCY MUSTER POINT ROLL CALL SHEET.....	79
10.7 ANNEXURE G – EMERGENCY RESPONSE - IN CASE OF FIRE	79
10.8 ANNEXURE H – EMERGENCY ACTION PLAN	79
10.9 ANNEXURE I – EMERGENCY DRILL PLAN	79
10.10 ANNEXURE J – PROJECT EMERGENCY RESPONSE COMMUNICATION CHART	79
10.12 ANNEXURE L – FIRST AID KIT INSPECTION CHECKLIST	79
10.11 ANNEXURE K – EMERGENCY RESPONSE TEAM.....	79
10.11 ANNEXURE K – EMERGENCY TOOLS AND EQUIPMENTS.....	79
10.11 ANNEXURE K – FIRE RISK/ IMPACT ASSESSMENT	79

SECTION 1 – GENERAL

This Emergency Preparedness and Response Plan (EPRP) is developed in alignment with the approved Emergency / Contingency & Business Continuity Plan (ECBCP) and provides project-specific emergency preparedness and response arrangements for Project R1181/2 – Improvement of Al Sufa Road.

This Plan adopts the Plan–Do–Check–Act (PDCA) methodology to ensure systematic implementation, monitoring, and continual improvement of emergency preparedness and response capability throughout the project lifecycle.

1.1 INTRODUCTION – PDCA BASED APPROCH

SL. NO.	PDCA PHASE	DESCRIPTION	APPLICATION FOR R1181/2
1	PLAN	Establish objectives, identify hazards, assess risks, and define emergency procedures.	Identification of risks & foreseeable emergencies, assignment of roles/responsibilities, resource planning, procedure development, communication planning.
2	DO	Implement the planned controls and execute procedures.	Training of personnel, conducting drills, implementing emergency response actions during incidents.
3	CHECK	Monitor, measure, audit and evaluate performance against requirements.	Mock drills, internal/external audits, KPI monitoring, incident investigation and lessons learned.
4	ACT	Take corrective actions and continuously improve the plan.	Review findings, update EPRP, implement preventive measures, improve resilience across all project stages.

1.2 SCOPE OF THE EPRP

Scope of Applicability:

This EPRP applies to all project activities, locations, personnel, subcontractors, consultants, RTA representatives, and stakeholders. It addresses all foreseeable emergency scenarios, including but not limited to:

SL. NO.	CATEGORY	COVERAGE
1	Personnel	All CCECC employees, subcontractors, consultants, RTA personnel, and visitors
2	Locations	Construction zones, site offices, laydown areas, traffic diversions, and welfare facilities
3	Project Phases	Mobilisation, Construction, Testing & Commissioning, Handover, Defects Liability Period
4	Foreseeable Emergencies	Fire/explosion, excavation collapse, falls from height, utility strikes, major traffic incidents, medical emergencies, environmental spills, extreme weather, infectious diseases

The Plan ensures protection of life, health, the environment, assets, and minimises disruption and project delays.

1.3 APPROVAL OF THE PROJECT EMERGENCY PREPAREDNESS AND RESPONSE PLAN

This process ensures that the EPRP remains accurate, authorised, current, and traceable.

SL. NO.	PREPARED BY	REVIEWED BY	APPROVED BY
1	HSE Engineer	Project HSE Manager / Deputy Project Manager	Project Director

Note: Approval confirms management’s commitment to resource allocation, training, and continual improvement of emergency preparedness and response arrangements throughout the project lifecycle. Signed approval sheets are provided on **Page 02**.

1.4 DOCUMENT CONTROL AND VERSION MANAGEMENT

SL. NO.	REQUIREMENT	DESCRIPTION
1	Distribution	Latest approved version displayed on site notice boards and available on the project shared drive
2	Revision Control	All revisions recorded in the Revision Register
3	Obsolete Documents	Removed immediately from circulation and archived
4	Communication	Changes communicated via toolbox talks and induction refreshers, where required

This section lists commonly used abbreviations and their definitions for clarity and consistent understanding throughout this HSE Plan.

1.5 ABBREVIATIONS AND DEFINITIONS

1.5.1 ABBREVIATIONS

SL. NO.	ABBREVIATION	FULL FORM	RELEVANCE
1	PDCA	Plan–Do–Check–Act	Continual improvement methodology
2	EPRP	Emergency Preparedness and Response Plan	This document
3	ERT	Emergency Response Team	Initial on-site responders
4	EMT	Emergency Management Team	Strategic coordination
5	RTO	Recovery Time Objective	Acceptable downtime for critical operations
6	HSE	Health, Safety & Environment	All emergency phases

1.5.2 DEFINITIONS (KEY TERM)

SL. NO.	TERM	DEFINITION
1	Emergency	A serious, unexpected, and potentially dangerous situation requiring immediate action to protect life, property, the environment, or operations

1.6 REFERENCE DOCUMENTS AND STANDARDS

The CLMP is prepared in accordance with the following project, regulatory, and international standards:

SL. NO.	REFERENCE	DOCUMENT / STANDARD
1	RTA	QHSS MSTG C.9 – Project Emergency / Contingency & Business Continuity Planning
2	NCEMA	UAE National Emergency Management Guidelines
3	UAE Fire Safety Code	Fire and Life Safety Code of Practice – 2018
4	UAE Federal Law	Federal Decree Law No. 2 of 2011
5	RTA	Work Zone Traffic Management Manual – 2018
6	Dubai Municipality	Applicable codes and standards
7	ISO	ISO 45001 (OH&S), ISO 22301 (Business Continuity)
8	Project Documents	HSEM Plan, Risk Assessments, TMP, Traffic Guidelines
9	RTA Circulars	Nos. 7, 18, 33, 41, 42, 44
10	Dubai Civil Defence	Law No. (4) of 2025

SECTION 2 – PROJECT DETAILS

This section provides an overview of Project R1181/2 – Improvement of Al Safa Road, including the project scope, key activities, locations, stakeholders, manpower, and site-specific constraints relevant to emergency planning and response. The information in this section establishes the operational context for identifying foreseeable emergencies and implementing appropriate emergency management measures.

2.1 PROJECT SCOPE OF WORK (EMERGENCY RELATED)

The R1181/2 project involves the comprehensive improvement and upgrading of Al Safa Road and its associated corridors, including road widening, new pavement layers, utility relocation/diversion, drainage upgrades, street lighting, traffic signals, landscaping, tunnel/bridge construction, and associated civil/infrastructure works.

2.2 PROJECT OVERVIEW

SL. NO.	ACTIVITY	DESCRIPTION
1	Roadwork	Road widening, pavement construction
2	Utility Works	Relocation/diversion of DEWA power/water, Etisalat/Du fibre, gas, chilled water
3	Drainage	Upgrades, flood prevention measures
4	Electrical	Street lighting, traffic signal installation
5	Structures	Tunnels, bridges, ramps
6	Traffic Management	Temporary and permanent traffic diversions

2.3 FORESEEABLE EMERGENCIES – PROJECT RISK CONTEXT

Due to the urban, high-traffic location and complexity of works, the following foreseeable emergencies have been identified in the Project Risk Register (Ref: R1181/2-HSE-RA). These form the basis of this Emergency Management Plan.

SL. NO.	ASPECT OF SCOPE	KEY EMERGENCY RELEVANCE	L	S
1	Fire / Explosion	Hot works, fuel storage, temporary offices	High	Major
2	Excavation Collapse	Deep excavations, shoring, heavy lifting	High	Catastrophic
3	Fall From Height	Scaffolding, MEWPs, bridge edges	High	Major
4	Utility Strikes	Mechanical excavation near live utilities	Very High	Catastrophic
5	Traffic Incidents	Night works, lane closures, plant crossing	High	Major
6	Medical Emergencies	Heat stress, heavy lifting	High	Major
7	Environmental Spills	Fuel, oil, bitumen, chemicals	Medium	Major
8	Extreme Weather	Sandstorms, flooding	Medium	Major
9	Pandemic	High workforce density	Low-Medium	Major

2.4 EPRP OBJECTIVES


A fully compliant, site-specific response framework that satisfies RTA MSTG C.9 and ensures:

SL. NO.	ACTIVITY	DESCRIPTION
1	Life Safety	Prevent fatalities and major injury
2	Public Protection	Ensure safety of road users and pedestrians
3	Asset / Environmental Protection	Minimise damage to property and environment
4	Operational Recovery	Rapid reinstatement of activities
5	Regulatory Compliance	Full adherence to RTA, DCD, DM, NCEMA requirements

2.5 PROJECT IDENTIFICATION

SL. NO.	ITEM	DETAILS
1	Project Name	R1181/2 – Improvement of Al Safa Road
2	Client	Roads & Transport Authority (RTA)
3	Consultant	Parsons Overseas Limited
4	Main Contractor	CCECC – Dubai Branch
5	Duration	18 Sep 2025 – 18 Mar 2028
6	Locations	Al Safa Road and connecting corridors

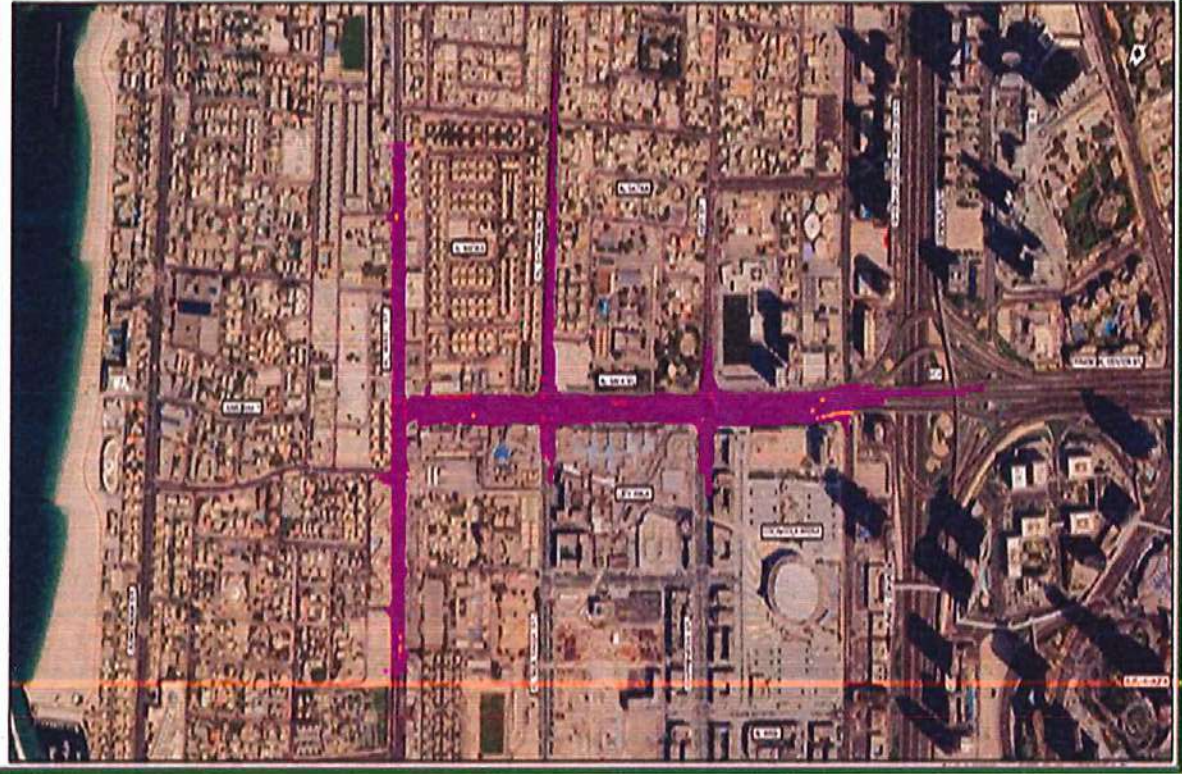

SL. NO.	ITEM	DETAILS
	 Precise Project Layout Plan – Drawing No. RTA100003-POL-HGN-R11812-DR-HE-000201 provided by the Consultant	

2.6 PROJECT KEY PERSONNEL AND EMERGENCY CONTACT NUMBERS

SL. NO.	ROLE	NAME	EMAIL	CONTACT NO.
1	Project Director	Mohsen D. Gazzaz	mohsen.gazzaz@cceccdubai.com	+971 52 282 5807
2	Deputy PM	Ahmed Elkadi	ahmed.elkadi@cceccdubai.com	+971 50 907 0342
3	Deputy PM	Guo Pengcheng	guo.pengcheng@cceccdubai.com	+971 58 103 0678
4	Construction Manager	Ahmed Shekhar Ghanem	as.ghanem@ccecc.ae>	+971 52 4223948
5	Construction Manager	Shi Enji	enji.shi@cceccdubai.com	+971 54 7381666
6	PHSEM	Mirza Shahabuddin Baig	mirza.shahabuddin@cceccdubai.com	+971 55 933 1082
7	Emergency Response Coordinator	Ajmal Rashid	ajmal@ccecc.ae	+971 56 148 7012
8	Kasim Muhammad	Sr. Utility Engineer	kasim.mohammad@ccecc.ae	+971 56 1435466

SL. NO.	ROLE	NAME	EMAIL	CONTACT NO.
9	Hasim Ali	Civil Engineer	hashim.ali@ccecc.ae	+971 55 2889793
Emergency				
10	Police	999	Law Enforcement	
11	Ambulance	998	Medical	
12	Fire / Civil Defence	997	Fire / Rescue	
13	DEWA Emergency	991	Water and Electricity	
14	Dubai Municipality	800 900	Sewage water + others	
15	RTA Emergency Control Room	800 9090 / 04 284 4444		

This contact list shall be displayed at all site offices, emergency boards, and security gates and reviewed quarterly.

2.7 SITE CONSTRAINTS AFFECTING EMERGENCY RESPONSE

SL. NO.	CONSTRAINT	IMPACT ON EMERGENCY RESPONSE	MITIGATION ALREADY IN PLACE
1	Extremely high live traffic volumes	Delays emergency vehicle access	Dedicated emergency lanes in all TMP stages
2	Residential areas, schools, mosques	Large pedestrian movement, difficult evacuation	Pre-identified safe assembly points away from traffic
3	Deep excavations & multiple work fronts	Risk of collapse, difficult rescue	24/7 standby rescue team & equipment
4	Numerous live utilities	High risk of utility strike	Permit-to-dig system, CAT-4 scanners, utility coordinators
5	Flash flood risk	Rapid water ingress into excavations	Dewatering pumps on 24 h standby, flood barriers
6	Night works	Reduced visibility, fatigue	Floodlights, reflective signage, additional supervision

SECTION 3 – INTRODUCTION, PURPOSE, SCOPE & COMMITMENT OF EPRP

This section defines the purpose and scope of the Emergency Preparedness and Response Plan (EPRP) and confirms CCECC management's commitment to effective emergency preparedness, response, and continual improvement in accordance with PDCA principles and applicable regulatory requirements.

3.1 PURPOSE OF THE EPRP

This Emergency Preparedness and Response Plan (EPRP) has been developed specifically for Project R1181/2 – Improvement of Al Safa Road to satisfy the requirements of RTA MSTG C.9 – Project Emergency / Contingency & Business Continuity Planning, and to establish a structured framework for managing foreseeable emergency situations.

SL. NO.	PURPOSE AREA	DESCRIPTION
1	Life Safety	Protect the workforce, subcontractors, consultants, RTA personnel, and members of the public
2	Property Protection	Reduce damage to assets, plant, equipment, and infrastructure
3	Environmental Protection	Prevent spills, contamination, and ecological harm
4	Business Continuity	Minimise operational disruption and ensure rapid recovery
5	Legal Compliance	Fulfil applicable requirements of RTA MSTG C.9, DCD, DM, NCEMA, and UAE legislation

3.2 SCOPE OF THE PLAN

This EPRP applies to:

SL. NO.	CATEGORY	INCLUDED IN SCOPE
1	Work Areas	Construction zones, offices, laydown yards, welfare areas
2	Personnel	Employees, subcontractors, consultants, RTA staff, visitors
3	Project Phases	Mobilization → Construction → Handover → Defects Liability Period

3.3 MANAGEMENT COMMITMENT & PDCA APPLICATION

CCECC senior management is fully committed to the effective implementation of this Emergency Preparedness and Response Plan (EPRP) in alignment with RTA MSTG C.9, ISO 45001, and ISO 22301 requirements. Adequate resources—including competent personnel, training, equipment, and funding—will be provided to ensure emergency preparedness, effective response, and continual improvement.

The project applies the Plan–Do–Check–Act (PDCA) methodology to manage emergency preparedness and response as follows:

SL. NO.	PHASE	PROJECT APPLICATION
1	Plan	Hazard identification, risk assessment, emergency scenario development, resource planning, procedure development, training needs analysis.
2	Do	Implementation of emergency procedures, conducting drills, maintaining equipment, real event response.
3	Check	Monitoring, inspections, performance KPIs, audits, drill performance review, incident investigation.
4	ACT	Lessons learned, corrective & preventive actions, plan updates, continuous improvement.

SECTION 4 –EMERGENCY RESPONSE PLANING (PLAN PHASE- PDCA)

The Planning Phase defines all foreseeable emergency scenarios, required resources, designated responsibilities, communication protocols, and preparedness measures necessary to ensure an effective emergency response for Project R1181/2 – Improvement of Al Safa Road.

This section aligns with RTA MSTG C.9, ISO 45001:2018, ISO 22301:2019, and NCEMA emergency planning requirements.

4.1 PLANNING OBJECTIVES

SL. NO.	OBJECTIVE	TARGET / KPI	ACCOUNTABILITY	TIMEFRAME
1	Complete hazard identification for all project work activities	100% coverage of method statements, risk assessments, and risk register	Project HSE Manager	Pre-mobilisation and Every month review and update the Risk Register
2	Assess and prioritise all foreseeable emergency scenarios (9 scenarios)	Risk ratings documented and approved (Ref: R1181/2-HSE-RA)	HSE Team / Risk Committee including Construction Manager	Within 14 days of any scope or methodology change
3	Establish ALARP controls for all high and very-high-risk activities	All high and very-high risks reduced to ALARP level per risk matrix	Deputy Project Manager	Ongoing, verified monthly
4	Define emergency roles and ensure competency of key personnel	100% role coverage; all ERT members trained and certified	Emergency Coordinator	At induction and annual refresher
5	Coordinate with external emergency response agencies (RTA, Civil Defence, DEWA, DM)	Formal coordination established; emergency contact lists validated	Project Director	Pre-construction and bi-annual review

4.2 EMERGENCY HAZARD IDENTIFICATION, PRIORITY & ALARP CONTROLS

This table identifies potential emergency scenarios and their causes, assigns risk-based priorities, specifies ALARP controls, and describes how risks are managed through systems such as Risk Assessments, Permit to Work (PTW), and approved plans.

SL. NO.	SCENARIO	CAUSE OF SCENARIO	PRIORITY	ALARP CONTROLS	CONTROL MEASURES	RESPONSIBLE	STATUS
1	Fire & Explosion	Hot works, bitumen heating, fuel storage, electrical faults, generator use	High	Hot work permit, fire watch, fire extinguishers, safe fuel storage, emergency shutdown	Risk Assessment, Hot Work PTW, Fire Emergency Plan, Firefighting Training, Equipment Inspection	Project HSE Manager & Supervisors	Implemented
2	Excavation & Temporary Works Collapse	Deep excavations (up to 8 m), inadequate shoring, soil instability, water ingress	Very High	Approved shoring design, daily inspection, access control, rescue equipment standby	Risk Assessment, Excavation PTW, Temporary Works Design, Inspection Checklist, Rescue Plan	Construction Manager & HSE Manager	Implemented
3	Fall from Height & Suspension Trauma	Work on scaffolds, MEWP operations, bridge edges	High	Harnesses, guardrails, rescue plan, trained operators	Risk Assessment, Work-at-Height PTW, Method Statement, Height Rescue Plan, Training	Site Engineer & HSE Officer	Implemented
4	Utility Strike	Mechanical excavation near live utilities, inaccurate drawings, HDD works	Very High	Permit-to-dig, CAT-4 scanning, hand digging within 1 m, utility coordinator	Risk Assessment, Permit-to-Dig System, Utility Drawings, Isolation Plan, Emergency ERP	Utility Coordinator & Electrical Engineer	Ongoing
5	Major Traffic Incident	Live traffic diversions, plant crossing, night works, public intrusion	High	Approved TMP, emergency lanes, trained traffic marshals, police coordination	Traffic Risk Assessment, TMP Approval, RTA Permit, Traffic Emergency Plan	Traffic Manager	Ongoing
6	Medical Emergency & Heat Stress	Prolonged outdoor work, extreme heat, dehydration, fatigue	High	First aiders, shaded rest areas, hydration, work-rest regime, AED	Risk Assessment, Heat Stress Plan, Medical Emergency Procedure, Toolbox Talks	HSE Manager & Site Nurse	Implemented
7	Environmental Spill	Fuel refuelling, oil leakage, bitumen handling, concrete washout	Medium	Spill kits, trained spill team, drain protection, controlled refuelling	Environmental Risk Assessment, Spill Response Plan, MSDS, Inspection Checklist	HSE Officer & HSE Engineer	Implemented

SL. NO.	SCENARIO	CAUSE OF SCENARIO	PRIORITY	ALARP CONTROLS	CONTROL MEASURES	RESPONSIBLE	STATUS
8	Extreme Weather (Flood & Sandstorm)	Heavy rain causing flooding, sandstorm reducing visibility	Medium	Weather monitoring, dewatering pumps, work stoppage, evacuation plan	Weather Risk Assessment, Emergency Weather Plan, Dewatering Plan	Emergency Coordinator	Implemented
9	Pandemic / Infectious Disease	Workforce density, shared transport, accommodation	Low-Medium	Health screening, isolation, hygiene controls	Risk Assessment, Pandemic Response Plan, DHA Guidelines	Project Manager + Male Nurse	Implemented
10	Rescue Confined Space (manholes, chambers, ducts)	Injury, gas exposure, collapse, water ingress	Very High	Entry controls, rescue team, equipment	CSE PTW, CSE Procedure, Rescue Plan	CSE Supervisor / HSE	Implemented

4.3 FORESEEABLE EMERGENCY SCENARIOS SUMMARY

SL. NO.	FORESEEABLE SCENARIO	SCENARIO RAISED DUE TO	RISK PRIORITY	RESPONSE STRATEGY
1	Fire / Explosion	Unsafe hot work activity performed, unsafely storage of fuel, unsafe electrical connection and lack of smoking policy.	High	Major injury, asset damage
2	Excavation Collapse	Unsafe Deep excavation benching, sloping or shoring failure, failure of Dewatering resulting water ingress	Very High	Fatality, multiple casualties
3	Fall from Height	MEWP is being use inappropriately, unsafe scaffolding platform, working on bridge erection	High	Serious injury or fatality
4	Utility Strike	Excavation being performed near live utilities without following the appropriate procedure.	Very High	Explosion, electrocution
5	Traffic Incident	Inadequate work zone protection adjacent to Live traffic works, unsafe diversion made and lane closures inadequate system or by incompetent operatives.	High	Public injury, traffic disruption
6	Medical / Heat Stress	Working in Extreme heat without taking adequate hydration precaution, physical exertion	High	Severe illness or fatality
7	Environmental Spill	Unsafely handling and storage of fuel and chemicals resulting spillage and unsafe refuelling.	Medium	Environmental damage

 دولة فلسطين STATE OF PALESTINE	 PARSONS	 中国土木 CCECC
CHINA CIVIL ENGINEERING CONSTRUCTION CORPORATION–Dubai Branch		
R1181/2 Emergency Preparedness and Response Plan (EPRP)		
Doc. Ref:	CCECC-R1181/2- PEPR-PLN-07	
Rev. No.:	00	
Date:	09 December 2025	

SL. NO.	FORESEEABLE SCENARIO	SCENARIO RAISED DUE TO	RISK PRIORITY	RESPONSE STRATEGY
8	Extreme Weather	Heavy rain, poor visibility	Medium	Flooding, work stoppage
9	Rescue from Confined Space	Incident inside manholes / chambers	Very High	Asphyxiation, fatality
10	Rescue from Mobile / Crawler Crane Emergency	Collapse of crane	High	Trapped man force
11	Pandemic	Workforce density, shared facilities	Low– Medium	Workforce disruption

4.4 EMERGENCY SCENARIO-WISE PLANNED RESPONSE STRATEGY (PLAN PHASE)

This table explains what will be done, by whom, and what the first priority is, for each foreseeable emergency.

SL. NO.	EMERGENCY SCENARIO	PRIMARY RESPONSE STRATEGY (PLANNED)	PRIORITY ACTION	LEAD ROLE	STATUS
1.	Fire / Explosion	Immediate alarm, evacuation, fire suppression	Life safety first	ERT Leader	Planned
2.	Excavation Collapse	Stop work, rescue deployment, stabilize excavation	Rescue & scene safety	Rescue Team Lead	Planned
3.	Fall from Height	Secure casualty, prevent suspension trauma, medical aid	Casualty recovery	Height Rescue Team	Planned
4.	Utility Strike	Stop work, isolate utility, cordon area	Prevent escalation	Utility Coordinator –	Planned
5.	Major Traffic Incident	Secure scene, divert traffic, protect public	Public safety	Traffic Manager	Planned
6.	Medical / Heat Stress	Immediate first aid, cooling, ambulance	Medical stabilization	HSE Manager + Site Nurse	Planned

		
CHINA CIVIL ENGINEERING CONSTRUCTION CORPORATION–Dubai Branch R1181/2 Emergency Preparedness and Response Plan (EPRP)		
Doc. Ref: CCECC-R1181/2- PEPR-PLN-07 Rev. No.: 00 Date: 09 December 2025		

SL. NO.	EMERGENCY SCENARIO	PRIMARY RESPONSE STRATEGY (PLANNED)	PRIORITY ACTION	LEAD ROLE	STATUS
7.	Environmental Spill	Contain spill, protect drains, notify authorities	Environmental protection	HSE Officer	Planned
8.	Extreme Weather	Stop work, evacuate low areas, deploy pumps	Personnel safety	Emergency Coordinator (CM)	Planned
9.	Rescue from Confined Space	Life rescue	Non-entry rescue, trained team	CSE Rescue Lead	Planned
10.	Pandemic	Isolate affected personnel, follow DHA protocol	Infection control	HSE Manager + Site Nurse	Planned

4.5 ROLES & RESPONSIBILITIES – EMERGENCY PLANNING DUTIES (PLAN PHASE)

This subsection defines who plans what, who controls what, and who has authority during emergency preparedness. It ensures clarity of responsibility before an emergency occurs,

SL. NO.	ROLE	PLANNING RESPONSIBILITIES (PLAN PHASE)	AUTHORITY LEVEL	REQUIRED COMPETENCY / TRAINING	STATUS
1	Project Director	Approve Emergency Management Plan, allocate resources, coordinate with RTA & authorities	Final authority	Leadership in Crisis Management	Implemented
2	Deputy Project Manager	Support planning, ensure resources availability, oversee construction-related emergency risks	Site-wide authority	Incident Command System (ICS) awareness	Implemented
3	Project HSE Manager	Develop EMP, maintain risk register, define ALARP controls, ensure compliance	Authority to stop unsafe work	NEBOSH / Safety Diploma, Emergency Planning	Implemented
4	Emergency Response Coordinator	Develop ERPs, plan drills, maintain emergency contacts and communication flow.	Activate ERT	Emergency Coordination & Command Training	Implemented
5	Construction Manager	Plan emergency resources (pumps, cranes, lighting), ensure constructability safety	Resource control	Construction Emergency Awareness	Implemented
6	Traffic Manager	Plan emergency traffic diversions, maintain emergency lanes in TMP	TMP modification authority	RTA TTM Certification	Ongoing

		 
CHINA CIVIL ENGINEERING CONSTRUCTION CORPORATION—Dubai Branch R1181/2 Emergency Preparedness and Response Plan (EPRP)		Doc. Ref.: CCECC-R1181/2- PEPR-PLN-07 Rev. No.: 00 Date: 09 December 2025

SL. NO.	ROLE	PLANNING RESPONSIBILITIES (PLAN PHASE)	AUTHORITY LEVEL	REQUIRED COMPETENCY / TRAINING	STATUS
7	Utility Coordinator	Plan utility isolation procedures, liaise with DEWA / Etisalat / DU / Gas	Utility isolation authority	Utility Safety & Permit Training	Ongoing
8	HSE Officer	Plan spill response, environmental protection measures	Spill response authority	Environment awareness Training	Implemented
9	Site Engineers / Supervisors	Plan task-level controls, ensure PTW & MS alignment	Task-level authority	PTW & Emergency Awareness	Implemented
10	ERT Leader	Plan ERT deployment, rescue readiness, equipment staging	On-site response authority	Fire & Rescue Certification	Implemented

4.6 EMERGENCY RESOURCES & EQUIPMENT PLANNING

What must already be available before an emergency

SL. NO.	RESOURCE CATEGORY	EQUIPMENT / RESOURCE	PLANNED LOCATION	AVAILABILITY	RESPONSIBLE	STATUS
1.	Fire Response	Fire extinguishers, fire blankets	Hot work zones, offices	24/7	Fire Warden	Implemented
2.	Rescue Equipment	Tripods, stretchers, rescue ropes	Excavation zones / ERT vehicle	24/7	ERT Leader	Implemented
3.	Medical	First aid kits, AED, trauma bags	First Aid Room / Site	Shift-based	Site Nurse	Implemented
4.	Flood Control	Dewatering pumps, Water tanker, Raincoat, Gum Boot, torch	Excavation areas	24/7	Site Engineer	Implemented
5.	Traffic Control	Cones, barriers, TMA VMS boards	Diversion areas	24/7	Traffic Manager	Ongoing
6.	Spill Response	Spill kits, absorbents	Fuel storage / plant yard	24/7	HSE Officer	Implemented
7.	Confined Space Rescue	Gas detector, tripod, winch	CSE areas	24/7	CSE Supervisor	Implemented

 دولة فلسطين STATE OF PALESTINE	 PARSONS [®]	 CCECC
CHINA CIVIL ENGINEERING CONSTRUCTION CORPORATION—Dubai Branch R1181/2 Emergency Preparedness and Response Plan (EPRP)		
	Doc. Ref:	CCECC-R1181/2- PEPR-PLN-07
	Rev. No.:	00
	Date:	09 December 2025

4.7 EMERGENCY COMMUNICATION, ESCALATION & ACCESS ROUTE PLANNING

This subsection defines how emergencies are communicated, how escalation occurs, and how emergency services reach the site and transport casualties to designated stations/hospitals, especially under live traffic conditions.

4.7 A – EMERGENCY COMMUNICATION & ESCALATION PLAN

SL NO.	COMMUNICATION TYPE	DESCRIPTION	METHOD	RESPONSIBLE PERSON	STATUS
1.	Initial Emergency Alert	Immediate notification of incident on site	Siren / Radio / Verbal	ERT Leader	Planned
2.	Internal Escalation	Inform Project Management & HSE	Phone / WhatsApp Emergency Group	Emergency Coordinator	Planned
3.	External Notification	Notify Police, Ambulance, Civil Defence	999 / 998 / 997	Emergency Coordinator	Planned
4.	Client / Consultant Notification	Inform RTA & Parsons	Official call / Email	Project Director	Planned
5.	Authority Coordination	Continuous updates during incident	Direct liaison	Emergency Coordinator	Planned
6.	Incident Documentation	Record timeline, actions, photos	Incident Log	HSE Coordinator	Planned

4.7 B – EMERGENCY ESCALATION LEVELS

SL NO.	INCIDENT LEVEL	DESCRIPTION	ESCALATION TO	CONTROL AUTHORITY
1.	Level 1 – Minor	First aid injury, small fire	ERT Leader	HSE Manager
2.	Level 2 – Serious	Injury, traffic impact, equipment damage	Project Director	Incident Commander
3.	Level 3 – Major	Fatality, collapse, utility strike	RTA / Police / Civil Defence	Incident Commander

 					
CHINA CIVIL ENGINEERING CONSTRUCTION CORPORATION—Dubai Branch R1181/2 Emergency Preparedness and Response Plan (EPRP)					
		Doc. Ref:	CCECC-R1181/2- PEPR-PLN-07		
		Rev. No.:	00		
		Date:	09 December 2025		
SL. NO.	INCIDENT LEVEL	DESCRIPTION	ESCALATION TO	CONTROL AUTHORITY	
4.	Level 4 – Disaster	Multiple casualties, public impact	NCEMA / DCDGC	RTA & Authorities	

4.8 EMERGENCY ROUT PLANNING (VEHICLE ACCESS & ASSEMBLY ACCESS)

This table explains how emergency vehicles will move through live traffic, reach the site, and transport casualties to designated stations and hospitals. All emergency muster points are pre-identified based on access, visibility, and distance from hazards.

4.8 A – EMERGENCY VEHICLE ACCESS & EXIT ROUTES

SL. NO.	EMERGENCY SERVICE	ACCESS ROUTE	EXIT ROUTE	CONTROL MEASURE	RESPONSIBLE
1	Ambulance	Emergency TMP lane	Nearest DHA hospital	Lane clearance	Traffic Manager
2	Fire / DCD	Approved corridor	Same route	Police coordination	Traffic Manager
3	Police	Live carriageway	As directed	TMP override	Incident Commander
4	Utility Emergency	Utility access points	Control station	Isolation zones	Utility Coordinator

4.8 B EMERGENCY ASSEMBLY POINTS & SITE LAYOUT

SL. NO.	EMERGENCY SERVICE	ACCESS ROUTE	EXIT ROUTE	CONTROL MEASURE
1	AP-01	Near Site Office	200 Persons	Good

		
CHINA CIVIL ENGINEERING CONSTRUCTION CORPORATION—Dubai Branch R1181/2 Emergency Preparedness and Response Plan (EPRP)		
Doc. Ref:	CCECC-R1181/2- PEPR-PLN-07	
Rev. No.:	00	
Date:	09 December 2025	

SL. NO.	EMERGENCY SERVICE	ACCESS ROUTE	EXIT ROUTE	CONTROL MEASURE
2	AP-02	Yard and store area	200 Persons	Good
3	AP-03	Al Wasl working area	200 Persons	Moderate
4	AP-04	Al Safa working area	200 Persons	Moderate
5	AP-05	Al Jumeriah working area	150 Persons	Good

4.9 EMERGENCY TRAINING & COMPETENCY PLANNING (PLAN PHASE – PDCA)

This subsection defines what emergency-related training is required, for whom, why it is required, and how competency will be ensured before any emergency occurs. It ensures that all personnel involved in emergency response are competent, trained, and authorised, in line with RTA MSG C.9, ISO 45001, ISO 22301, and NCEMA requirements.

4.9 A – EMERGENCY TRAINING NEEDS ANALYSIS & PLANNING MATRIX

SL. NO.	ROLE / POSITION	WHY TRAINING IS REQUIRED (EMERGENCY RISK)	REQUIRED TRAINING	PRIORITY	RESPONSIBLE PERSON	STATUS
1	Incident Commander (Project Director)	Overall command during major emergencies	Emergency Command & Crisis Management	High	Project Director	Planned
2	Deputy Incident Commander	Support and assume command when required	Incident Command System (ICS)	High	Deputy Project Manager	Planned
3	Project HSE Manager	Technical control, risk escalation, compliance	Emergency Planning & Incident Investigation	High	Project HSE Manager	Planned
4	Emergency Response Coordinator	Coordination, communication, authority liaison	Emergency Coordination & Communication	High	Emergency Coordinator	Planned

 حكومة دبي Government of Dubai		 中国土木 CCECC
CHINA CIVIL ENGINEERING CONSTRUCTION CORPORATION–Dubai Branch R1181/2 Emergency Preparedness and Response Plan (EPRP)		
Doc. Ref:		CCECC-R1181/2- PEPR-PLN-07
Rev. No.:		00
Date:		09 December 2025

SL. NO.	ROLE / POSITION	WHY TRAINING IS REQUIRED (EMERGENCY RISK)	REQUIRED TRAINING	PRIORITY	RESPONSIBLE PERSON	STATUS
5	ERT Leader	On-site emergency response leadership	Advanced Fire Fighting & Rescue	Very High	Emergency Coordinator	Planned
6	Fire Wardens	Fire suppression and evacuation support	Fire Warden & Extinguisher Training	High	HSE Officer	Planned
7	Rescue Team Members	Rescue from height, excavation, confined space	Rope Rescue / Confined Space Rescue	Very High	Rescue Supervisor	Planned
8	First Aiders / Site Nurse	Medical emergencies, heat stress	First Aid, BLS, AED	High	HSE Manager	Planned
9	Traffic Controllers	Traffic control during emergency	RTA Emergency TTM Training	Very High	Traffic Manager	Planned
10	Utility Isolation Team	Utility strike emergencies	Utility Isolation & Emergency Shutdown	Very High	Utility Coordinator	Planned
12	Supervisors / Foremen	Evacuation, muster control	Emergency Evacuation & Muster Control	High	HSE Officer	Planned

4.9B – EMERGENCY TRAINING FREQUENCY & COMPETENCY VALIDATION

SL. NO.	ROLE / POSITION	WHY TRAINING IS REQUIRED (EMERGENCY RISK)	REQUIRED TRAINING	PRIORITY
1	Emergency Command Training	Every 2 years	Certificate / Assessment	HSE Dept
2	Fire Warden Training	Annual	Practical assessment	HSE Dept
3	Rescue Training	Annual	Drill performance & certification	HSE Dept
4	First Aid / AED	Every 2 years	DHA-approved certificate	Medical Dept
5	Traffic Emergency TTM	As per RTA requirement	RTA certification	Traffic Dept
6	Utility Emergency Training	As required	Utility provider approval	Utility Coordinator

		
CHINA CIVIL ENGINEERING CONSTRUCTION CORPORATION—Dubai Branch R1181/2 Emergency Preparedness and Response Plan (EPRP)		
Doc. Ref:	CCECC-R1181/2- PEPR-PLN-07	
Rev. No.:	00	
Date:	09 December 2025	

SL. NO.	ROLE / POSITION	WHY TRAINING IS REQUIRED (EMERGENCY RISK)	REQUIRED TRAINING	PRIORITY
7	Emergency Awareness	Induction + annual	Attendance record	HSE Dept

4.9 C – EMERGENCY TRAINING PLANNING CONTROL

SL. NO.	CONTROL ELEMENT	DESCRIPTION	RESPONSIBLE PERSON	STATUS
1	Training Matrix	Role-based emergency training matrix	Project HSE Manager	Maintained
2	Training Schedule	Annual emergency training calendar	Emergency Coordinator	Planned
3	Attendance Tracking	Training attendance and validity	HSE Officer	Maintained
4	Competency Review	Review after drills/incidents	Project HSE Manager	Ongoing
5	Refresher Training	Based on performance gaps	Emergency Coordinator	Planned

4.10 EMERGENCY DRILL PLANNING (LINK TO DO & CHECK PHASES)

This subsection defines which drills will be conducted, why, and how often, as part of preparedness planning.

Emergency Drill Planning Matrix

SL. NO.	DRILL TYPE	WHY REQUIRED	FREQUENCY	LEAD ROLE	PRIORITY	STATUS
1.	Fire Drill	Validate fire response & evacuation	Monthly	ERT Leader	High	Planned
2.	Excavation Collapse Drill	Test rescue readiness	Quarterly	Rescue Team Lead	Very High	Planned
3.	Traffic Incident Drill	Public & vehicle safety	Quarterly	Traffic Manager	Very High	Planned
4.	Utility Strike Drill	Isolation & escalation	Bi-monthly	Utility Coordinator	Very High	Planned
5.	Medical / Heat Stress Drill	Medical response readiness	Monthly	Site Nurse	High	Planned
6.	Confined Space Rescue Drill	Rescue capability	6 Monthly	CSE Supervisor	Very High	Planned
7.	Extreme Weather Drill	Flood / sandstorm preparedness	Annual / Seasonal	Emergency Coordinator	Medium	Planned

		
CHINA CIVIL ENGINEERING CONSTRUCTION CORPORATION–Dubai Branch R1181/2 Emergency Preparedness and Response Plan (EPRP)		Doc. Ref.: CCECC-R1181/2- PEPR-PLN-07 Rev. No.: 00 Date: 09 December 2025

FORESEEABLE INCIDENTS & EMERGENCY RESPONSE SUMMARY

to be read in conjunction with Standard Emergency Response Procedure

SL. NO.	DRILL TYPE	WHY REQUIRED	KEY ACTIONS SUMMARY FREQUENCY	RESPONSIBLE ERT ROLES	RESCUE EQUIPMENT REQUIRED	TRAINING REQUIRED
1.	Fire on Land (Site / Office / Plant)	Level 1–4	Raise alarm, evacuate, firefighting if safe, emergency services	Fire Warden, ERT Leader	Fire extinguishers, PPE, stretcher	Fire Warden, Fire Safety
2.	Excavation Collapse / temporary work collapse	Level 2–4	Evacuate area, headcount, manual rescue only, emergency services	Rescue Team, Site Supervisor	Hand tools, stretcher, AED	Excavation Safety, Rescue
3.	Suspension Trauma (Rescue from Height)	Level 3	Immediate rescue to remove load, stabilize casualty, medical evacuation	ERT Leader, First Aider, Height Rescue Team	Rescue stretcher, spinal collar, oxygen, AED, first aid kit	WAH Rescue, First Aid
4.	Utility Strike (Electric / Gas / Water / Fibre)	Level 1–4	Stop work, isolate utility, secure area, emergency services if required	Utility Coordinator, ERT	Insulated tools, AED, first aid kit	Utility Safety, Electrical Awareness
5.	Traffic Incident (Project / Public Vehicle)	Level 1–4	Secure scene, traffic control, casualty care	Traffic Manager, First Aider	Traffic cones, stretcher, first aid kit	TTM, First Aid
6.	Medical Emergency / Incapacitated Person	Level 1–3	First aid, stabilize, medical evacuation if required	First Aider, Site Nurse	First aid kit, AED, stretcher	First Aid, BLS
7.	Environmental Spill (Land / Marine)	Level 1–4	Stop source, contain spill, protect drains, notify authorities	Environmental Team, ERT	Spill kits, booms, PPE	Spill Response, Chemical Awareness

						
CHINA CIVIL ENGINEERING CONSTRUCTION CORPORATION—Dubai Branch						
R1181/2 Emergency Preparedness and Response Plan (EPRP)						
		Doc. Ref: CCECC-R1181/2- PEPR-PLN-07				
		Rev. No.: 00				
		Date: 09 December 2025				
SL. NO.	DRILL TYPE	WHY REQUIRED	KEY ACTIONS SUMMARY FREQUENCY	RESPONSIBLE ERT ROLES	RESCUE EQUIPMENT REQUIRED	TRAINING REQUIRED
8.	Extreme weather Heat Stress / Heat Stroke	Level 2–4	Move to shade, cooling, hydration, medical support	First Aider, Supervisor	First aid kit, stretcher	Awareness on sandstorm. Heat Stress Awareness, First Aid
9.	Confined Space Rescue (Manholes, Chambers)	Level 2–4	Non-entry rescue where possible, gas monitoring, trained entry only if safe	CSE Rescue Team, ERT Leader	Tripod, winch, gas monitor, BA, stretcher	Confined Space Rescue, BA, First Aid
10.	Rescue from Mobile / Crawler Crane Cabin	Level 3–4	Rescue using approved height rescue system, medical evacuation	Rescue Team, First Aider	Rescue ropes, stretcher, oxygen	Height Rescue, First Aid
11.	Pandemic / Infection	Level 2–3	isolation	Male nurse	Mask,	Pandemic / infection

SECTION 5 – EMERGENCY PREPAREDNESS IMPLEMENTATION (DO PHASE)

This section operationalizes the emergency planning from Section 4 (PLAN) through systematic site-level execution on Project R1181/2, deploying trained Emergency Response Teams (ERT), activating ERP-P01 to ERP-P11 procedures, ensuring resource availability, conducting drills, and maintaining workforce readiness for effective incident response.

Key Execution Elements

Emergency arrangements are made fully operational via trained personnel deployment, resource mobilization, procedure implementation, and continuous communication, aligning with RTA MSTG, ISO 45001, and PDCA "DO" requirements for visible, audit-ready performance.

This phase guarantees all controls and responsibilities from planning are actively executed across mobilization, construction, and demobilization phases.

5.1 IMPLEMENTATION OF OBJECTIVES

Sl. No.	IMPLEMENTATION OBJECTIVE	TARGET / KPI	ACCOUNTABILITY	FREQUENCY / TIMEFRAME
1.	Deploy all emergency equipment and ensure operational readiness	100% functionality verified (checklists signed)	Emergency Coordinator / ERT Leader	Weekly verification
2	Conduct emergency communication testing (radio, siren, call chain)	100% response within 2 minutes	Emergency Coordinator	Monthly
3	Ensure all trained personnel occupy designated emergency roles	100% ER team members verified on shift	Project Manager HSE	Before work start daily
4	Display updated emergency contacts and procedures at site notice boards	All locations covered	HSE Officer	Weekly
5	Implement toolbox talks and awareness sessions on emergency response	Minimum 1 per week per crew	HSE Team	Weekly
6	Conduct emergency drills as per the Emergency Drill Matrix (Section 4.10)	100% planned drills executed and recorded	HSE Manager / Drill Lead	As per schedule
7	Coordinate emergency response with external agencies (RTA / DCD / DHA / DEWA)	Formal acknowledgment of coordination	Project Director	Bi-annual review

5.2 IMPLEMENTATION OF EMERGENCY RESPONSE PROCEDURES (ERPs)

The activation and execution of specific Emergency Response Procedures (ERP-P01 to ERP-P11) for all foreseeable emergencies from Section 4. These standardized procedures ensure consistent, role-based response during incidents on Project R1181/2 – Improvement of Al Safa Road.

Activation follows incident detection, escalation levels (Section 4.7B), and RTA MSTG C.9 / ISO 45001:2018 requirements.

ERP ACTIVATION & IMPLEMENTATION

Sl. No.	ERP REF	EMERGENCY SCENARIO	ACTIVATED BY	ON-SITE CONTROL	INITIAL ACTIONS	VERIFICATION
1.	ERP-P01	Fire & Explosion	Fire Warden / ERT Leader	Incident Commander	Alarm, evacuate, suppress; call 997	Fire log / extinguisher check
2	ERP-P02	Excavation / Temporary Works Collapse	Site Supervisor	Rescue Team Lead	Stop work, rescue, stabilize; shoring inspects	Rescue timeline / headcount
3	ERP-P03	Fall from Height / Suspension Trauma	Supervisor / First Aider	Height Rescue Lead	Secure casualty, rescue, medical; prevent trauma	Height rescue kit / medical log
4	ERP-P04	Utility Strike	Utility Coordinator	Incident Commander	Stop work, isolate, cordon; notify DEWA/DU	Isolation confirmation / perimeter log
5	ERP-P05	Major Traffic Incident	Traffic Manager	Incident Commander	Secure scene, divert traffic; RTA/police coord	TMP override / public safety report
6	ERP-P06	Medical Emergency / Heat Stress	First Aider / Site Nurse	HSE Manager	First aid, cool, ambulance; AED if needed	EMR Form / ambulance escort
7	ERP-P07	Environmental Spill	HSE Officer	HSE Engineer	Contain spill, protect drains; notify authorities	Spill kit log / waste disposal
8	ERP-P08	Extreme Weather (Flood / Sandstorm)	Emergency Coordinator	Incident Commander	Stop work, evacuate, pumps; weather monitor	Dewatering record / muster check
9	ERP-P09	Confined Space Rescue	CSE Supervisor	Rescue Team Lead	Non-entry rescue, gas test; ventilate	CSE PTW / tripod log
10	ERP-P10	Mobile / Crawler Crane Emergency	Lifting Supervisor	Incident Commander	Shutdown crane, secure area; rescue if trapped	Lifting PTW / crane inspection
11.	ERP-P11	Pandemic Infectious Disease Response Procedure	Admin / Welfare Team	HSE Manager	Isolate, screen, DHA protocol; hygiene enforces	Health screening / isolation log

5.3 ERP IMPLEMENTATION (EXECUTION) STEPS (COMMON FOR ALL)

Sl. No.	PROCEDURE	STEP	DESCRIPTION	RESPONSIBLE	TOOLS / RESOURCES	VERIFICATION
1.	Detection & Alert	Activate alarm; confirm type; Level 1 alert via siren / radio	Identify incident; activate nearest alarm	Any worker ERT Leader / Supervisor	Siren / Radio / Message	Alarm log
2.	Evacuation	Proceed to nearest AP; muster check; no re-entry until clear	Announce ERP ref + level via radio / WhatsApp	Activator Supervisors / Wardens	ERP checklist	Headcount report
3.	Scene Control	Isolate area; ensure safety; secure access	Execute priority actions (life safety first)	On-site control ERT / Scene HSE Officer	Section 4.6 equipment	Perimeter log
4.	Medical Response	Provide first aid; use ambulance route; log details	Notify per Level (4.7B); external if Level 3+	Emergency Coordinator Site Nurse / First Aiders	999 / 998 / 997 calls	EMR Form
5.	Communication	Escalate per levels; notify internals / externals	Secure scene, muster at AP (4.8B)	ERT Leader	Barriers / Traffic cones	Call chain record
6.	Resource Deployment	Deploy per Section 4.6; check function; log defects	All clear; debrief; CAPA if gaps	Incident Commander Equipment Custodian	Debrief form	Weekly checklist

ERP IMPLEMENTATION MONITORING

Sl. No.	MONITORING ELEMENT	CHECK FREQUENCY	KPI	RESPONSIBLE	CORRECTIVE ACTION
1.	ERP Availability	Weekly	100% accessible	HSE Engineer / DPM	Reprint / relocate
2.	Team Readiness	Daily shifts start	100% roles filled	Project Manager HSE	Backup assignment
3.	Drill Testing	Per 4.10 matrix	≤ Target time	Drill Lead	Retrain / re-drill
4.	Equipment Check	Weekly	100% functional	Equipment Custodian	Repair <24 hrs
5.	Records Completeness	Post-event	100% documented	HSE Coordinator	Audit / retrain

5.4 EMERGENCY DRILL EXECUTION

Drills verify the effectiveness of this implementation and build response readiness:

Sl. No.	DRILL TYPE	EXECUTION AUTHORITY	EXECUTION STEPS	DOCUMENTATION REQUIRED	VERIFICATION METHOD	KPI
1.	Fire Evacuation	ERT Leader	Alarm, evacuate, muster	Attendance Sheet, Drill Report Form	Assembly Time Evaluation	≤5 min assembly
2	Excavation Collapse	Rescue Lead	Simulate collapse, rescue	Drill Checklist, Photos	Time-to-Rescue Measurement	Time-to-rescue
3	Confined Space Rescue	CSE Supervisor	Non-entry rescue sim	Simulation Record, Debrief Report	Equipment Inspection Post-Drill	Equipment check
4	Traffic Incident	Traffic Manager	Secure scene, divert	Coordination Report with RTA	TMP Validation	Lane clearance
5	Medical / Heat Stress	Site Nurse	First aid sim, transfer	First Aid Performance Record	Peer Review	Stabilization time
6	Spill Response	HSE Officer	Contain, clean, dispose	Spill Log and Waste Disposal Record	Environmental Observation Sheet	Drain protection

5.5 COORDINATION WITH EXTERNAL AGENCIES

Sl. No.	AGENCY	IMPLEMENTATION ACTION	CONTACT PROTOCOL	RESPONSIBLE	STATUS CHECK
1.	Civil Defence (DCD)	Joint fire/rescue drills	997 call + liaison	Emergency Coordinator	Bi-annual
2	DHA Ambulance	Access route escort	998 call + route clear	Traffic Manager	Monthly test
3.	RTA/Traffic Police	Emergency lane override	TMP activation	Traffic Manager	Quarterly
4.	DEWA/ Etisalat / DU	Utility isolation support	Direct notify	Utility Coordinator	As needed
5.	All	Joint Interface Register updates (JEIR)	Meeting minutes	Project Director	Bi-annual

5.6 RECORDS & MONITORING

All implementation activities generate records to verify compliance:

Sl. No.	RECORD TYPE	PURPOSE	RESPONSIBLE	RETENTION	REVIEW FREQUENCY	RECORD TYPE
1.	Equipment Checklist	Functionality proof	HSE Officer	1 year	Weekly	Equipment Checklist
2	Drill Reports	Performance gaps	Emergency Coordinator	2 years	Monthly	Drill Reports
3	Incident Logbook	Timeline/actions	HSE Manager	2 years	Post-event	Incident Logbook
4	Training Sheets	Competency proof	HSE Officer	2 years	Monthly	Training Sheets
5	Communication Log	Test results	Emergency Coordinator	1 year	Monthly	Communication Log

5.7 PERFORMANCE MONITORING INDICATORS

Sl. No.	INDICATOR	TARGET	MONITORING TOOL	REPORTING FREQUENCY
1.	Emergency drill completion rate	100%	Drill Performance Log	Monthly
2	Response time from alarm to ERT activation	≤ 3 minutes	Drill Report Form	Monthly
3	Equipment readiness compliance	100% functional	Equipment Checklist	Weekly
4	Communication test success rate	100%	Communication Log	Monthly
5	Training validity coverage	100% current	Training Matrix	Monthly

5.8 CORRECTIVE ACTIONS

Sl. No.	GAP TYPE	ACTION	RESPONSIBLE	DEADLINE	FOLLOW-UP
1.	Equipment defect	Repair/replace	Custodian	24 hrs	Re-inspect
2	Drill failure	Retrain/drill	HSE Manager	7 days	Re-test
3.	Role vacancy	Assign/train	Coordinator	Immediate	Verify shift
4.	Communication fail	Test/fix system	Coordinator	48 hrs	Monthly test

		
CHINA CIVIL ENGINEERING CONSTRUCTION CORPORATION–Dubai Branch R1181/2 Project Emergency Preparedness and Response Plan (PEPRP)		Doc. Ref: CCECC-R1181/2-PEM-PLN-07 Rev. No.: 00 Date: 23 December 2025

SECTION 6 – MONITORING, MEASUREMENT, AUDIT & REVIEW (CHECK PHASE – PDCA)

This section outlines the monitoring, measurement, analysis, and evaluation processes to verify the effectiveness of emergency preparedness and response arrangements for Project R1181/2. It aligns with the "Check" phase of the PDCA methodology, RTA MSTG C.9 requirements for performance evaluation, ISO 45001:2018 (Clause 9), ISO 22301:2019, and NCEMA guidelines.

The CHECK phase evaluates the effectiveness of emergency preparedness and response arrangements implemented of Project R1181/2. under Sections 4 and 5.

It ensures that emergency controls, training, drills, communication systems, and resources are working as intended, remain compliant with RTA MSTG C.9, and are suitable for the evolving project risks.

The Check phase ensures objective evidence of implementation, identifies non-conformities, and provides data for continual improvement.

6.1 EMERGENCY PERFORMANCE MONITORING FRAMEWORK

Sl. No.	MONITORING ELEMENT	PURPOSE	MONITORING METHOD	RESPONSIBLE
1.	Emergency Response Effectiveness	Verify response capability	Drill observation & review	Project HSE Manager
2.	ERT Readiness	Confirm availability & competency	Attendance & deployment checks	Emergency Coordinator
3.	Equipment Readiness	Ensure emergency equipment works	Inspection records	Respective Owners
4.	Communication Effectiveness	Verify escalation flow	Drill simulation	Emergency Coordinator
5.	Compliance	Verify regulatory alignment	Internal audits	HSE Department

6.2 EMERGENCY DRILL EVALUATION & REVIEW

Sl. No.	DRILL TYPE	ERP REF	EVALUATION CRITERIA	EVIDENCE	RESPONSIBLE
1.	Fire Drill	ERP-P01	Alarm time, evacuation time, muster accuracy	Drill report	ERT Leader
2.	Excavation Collapse Drill	ERP-P02	Rescue time, coordination, safety	Drill report	Rescue Lead
3.	Traffic Incident Drill	ERP-P05	Scene control, public safety	Drill report	Traffic Manager
4.	Medical / Heat Stress Drill	ERP-P06	First aid response time	Drill report	Site Nurse
5.	Confined Space Rescue Drill	ERP-P09	Non-entry rescue effectiveness	Drill report	CSE Supervisor

Sl. No.	DRILL TYPE	ERP REF	EVALUATION CRITERIA	EVIDENCE	RESPONSIBLE
6	Extreme Weather Drill	ERP-P08	Evacuation & flood control	Drill report	Emergency Coordinator

6.3 INCIDENT & NEAR-MISS REVIEW

Sl. No.	EVENT TYPE	REVIEW ELEMENT	OUTPUT	RESPONSIBILITY
1.	Emergency Incident	Response adequacy	Improvement actions	Project HSE Manager
2	Near Miss	Potential escalation risk	Preventive actions	HSE Officer
3.	Property Damage	System failure	Corrective measures	Construction Manager
4.	Public Incident	TMP or access failure	TMP revision	Traffic Manager

6.4 EMERGENCY KPI MONITORING

Sl. No.	DRILL TYPE	ERP REF	EVALUATION CRITERIA	EVIDENCE	RESPONSIBLE
1.	Fire Drill	ERP-P01	Alarm time, evacuation time, muster accuracy	Drill report	ERT Leader
2	Excavation Collapse Drill	ERP-P02	Rescue time, coordination, safety	Drill report	Rescue Lead
3.	Traffic Incident Drill	ERP-P05	Scene control, public safety	Drill report	Traffic Manager
4.	Medical / Heat Stress Drill	ERP-P06	First aid response time	Drill report	Site Nurse
5.	Confined Space Rescue Drill	ERP-P09	Non-entry rescue effectiveness	Drill report	CSE Supervisor

6.5 EMERGENCY EQUIPMENT INSPECTION & VERIFICATION

SL. NO.	EQUIPMENT CATEGORY	INSPECTION FREQUENCY	VERIFICATION METHOD	RESPONSIBLE
1.	Firefighting Equipment	Monthly	Tag & checklist	Fire Warden
2	Rescue Equipment	Monthly / Pre-use	Visual & functional	ERT Leader
3.	Medical Equipment / AED	Weekly	Logbook	Site Nurse
4.	Spill Kits	Monthly	Inventory check	HSE Officer

SL. NO.	EQUIPMENT CATEGORY	INSPECTION FREQUENCY	VERIFICATION METHOD	RESPONSIBLE
5	Flood Control Equipment	Seasonal	Trial run	Construction Manager

6.6 TRAINING & COMPETENCY VERIFICATION

SL. NO.	REVIEW AREA	CHECK METHOD	ACCEPTANCE CRITERIA	RESPONSIBLE
1.	ERT Members	Drill performance	Competent	Emergency Coordinator
2	First Aiders	Certificate validity	In-date	HSE Manager
3.	Fire Wardens	Practical assessment	Pass	HSE Officer
4.	Traffic Team	RTA certification	Valid	Traffic Manager
5	Supervisors	Muster control assessment	Satisfactory	HSE Officer

6.7 COMMUNICATION & ESCALATION REVIEW

SL. NO.	REVIEW AREA	CHECK METHOD	ACCEPTANCE CRITERIA	RESPONSIBLE
1.	Alarm Activation	Drill observation	Immediate	ERT Leader
2	Internal Escalation	Simulation	Timely	Emergency Coordinator
3.	External Contact Accuracy	Contact list verification	Updated	HSE Coordinator
4.	Client Notification	Record review	Within SLA	Project Director

6.8 INTERNAL AUDIT & COMPLIANCE REVIEW

SL. NO.	REVIEW AREA	CHECK METHOD	ACCEPTANCE CRITERIA	RESPONSIBLE
1.	Internal HSE Audit	EPRP & ERP compliance	Quarterly	HSE Manager
2	Management Review	Emergency readiness	Bi-annual	Project Director

SL. NO.	REVIEW AREA	CHECK METHOD	ACCEPTANCE CRITERIA	RESPONSIBLE
3.	Consultant Audit	RTA MSTG C.9	As scheduled	Project Team
4.	Authority Inspection	Statutory compliance	As required	Project Director

6.9 INTERNAL AUDIT & COMPLIANCE REVIEW

SL. NO.	SOURCE	ACTION REQUIRED	TRACKING METHOD	RESPONSIBLE
1.	Drill Findings	Corrective action	Action tracker	HSE Manager
2.	Audit Findings	Preventive action	NCR register	Project HSE Manager
3.	Incident Review	System improvement	CAPA log	Construction Manager

6.10 OUTPUTS TO ACT PHASE

SL. NO.	OUTPUT FROM CHECK PHASE	INPUT TO ACT PHASE
1.	Drill performance gaps	Procedure updates
2.	Incident lessons learned	Corrective actions
3.	Audit findings	System improvement
4.	KPI trends	Management decisions

SECTION 7 – ACT - CORRECTIVE ACTION & CONTINUAL IMPROVEMENT

The ACT phase ensures that lessons learned from emergency incidents, drills, audits, inspections, and performance monitoring are systematically reviewed and used to improve emergency preparedness and response arrangements.

This phase closes the PDCA loop by implementing corrective actions, preventive actions, and continual improvement measures, ensuring the Emergency Preparedness and Response Plan (EPRP) remains effective, current, and aligned with project risks.

7.1 INPUTS TO THE ACT PHASE

SL. NO.	INPUT SOURCE	DESCRIPTION	RESPONSIBLE
1.	Emergency Incidents	Actual emergency response performance	Project HSE Manager
2.	Emergency Drills	Drill observations and gaps	Emergency Coordinator
3.	Near Miss Reports	Potential emergency escalation	HSE Officer
4.	Internal / External Audits	Compliance and system gaps	HSE Manager
5.	KPI Trends	Performance deviations	Project Director
6.	Authority / Consultant Feedback	Improvement requirements	Project Team

7.2 CORRECTIVE ACTION MANAGEMENT

Corrective actions are implemented to address **identified deficiencies**.

Sl. No.	NON-CONFORMANCE SOURCE	CORRECTIVE ACTION	RESPONSIBLE	TARGET DATE	STATUS
1.	Emergency Incident	Revise ERP / controls	Project Manager HSE	Defined per case	Tracked
2.	Drill Finding	Improve response time / coordination	Emergency Coordinator	Defined per drill	Tracked
3.	Audit Finding	Close compliance gaps	Respective Owner	Defined per NCR	Tracked
4.	Equipment Failure	Repair / replace equipment	Construction Manager	Immediate	Tracked

7.3 PREVENTIVE ACTION MANAGEMENT

Preventive actions are taken to **avoid recurrence** and reduce the likelihood of future emergencies.

Sl. No.	NON-CONFORMANCE SOURCE	CORRECTIVE ACTION	RESPONSIBLE	TARGET DATE	STATUS
1.	Delayed response	Additional training / drills	Emergency Coordinator	Drill review	Ongoing
2.	Equipment unavailability	Improve inspection regime	Equipment Owner	Inspection logs	Ongoing
3.	Communication gap	Update contact lists	HSE Coordinator	Verification checks	Ongoing
4.	New construction risks	Update risk register & EMP	Project HSE Manager	Risk review	Ongoing

7.4 UPDATE & REVISION OF EMERGENCY DOCUMENTS

SL. NO.	DOCUMENT	TRIGGER FOR UPDATE	RESPONSIBLE	APPROVAL AUTHORITY
1.	Emergency Preparedness and Response Plan (EPRP)	Incident, audit, scope change	Project HSE Manager	Project Director
2.	Emergency Response Procedures (ERP)	Drill outcome / incident	Emergency Coordinator	Project Director
3.	Risk Register	New or changed risk	HSE Manager	Deputy Project Manager
4.	Training Matrix	Competency gap	HSE Officer	Project HSE Manager

7.5 MANAGEMENT REVIEW & DECISION MAKING

Senior management reviews emergency preparedness performance and approves improvements.

SL. NO.	REVIEW ITEM	FREQUENCY	CHAIRPERSON	OUTPUT
1.	Emergency Performance	Bi-annual	Project Director	Improvement decisions
2.	Drill Effectiveness	Quarterly	Project HSE Manager	Action items
3.	Resource Adequacy	Bi-annual	Deputy Project Manager	Budget / procurement
4.	Compliance Status	Quarterly	Project Director	Compliance assurance

7.6 CONTINUAL IMPROVEMENT MECHANISM

SL. NO.	IMPROVEMENT AREA	IMPROVEMENT METHOD	RESPONSIBLE	STATUS
1.	Response Time	Enhanced drills	Emergency Coordinator	Ongoing
2.	Rescue Capability	Advanced rescue training	Rescue Supervisor	Ongoing
3.	Public Safety	TMP refinement	Traffic Manager	Ongoing
4.	Equipment Readiness	Preventive maintenance	Construction Manager	Ongoing

7.7 COMMUNICATION OF LESSONS LEARNED

SL. NO.	COMMUNICATION METHOD	TARGET AUDIENCE	RESPONSIBLE
1.	Toolbox Talks	Workforce	HSE Officer
2.	Safety Alerts	Site Management	Project HSE Manager
3.	Training Refreshers	ERT Members	Emergency Coordinator
4.	Management Briefings	Senior Management	Project Director

7.8 VERIFICATION OF ACT PHASE EFFECTIVENESS

SL. NO.	VERIFICATION METHOD	ACCEPTANCE CRITERIA	RESPONSIBLE
1.	Follow-up Audits	No repeat findings	HSE Manager
2.	Drill Re-evaluation	Improved performance	Emergency Coordinator
3.	KPI Review	Targets achieved	Project Director
4.	Incident Trends	Reduction in severity	HSE Department

7.9 PDCA CYCLE CLOSURE

SL. NO.	PDCA STAGE	OUT PUT
1.	PLAN	Emergency risks identified and controlled
2.	DO	Emergency response implemented
3.	CHECK	Performance evaluated
4.	ACT	System improved and updated

The completion of the ACT phase closes the PDCA cycle and feeds into the next planning cycle, ensuring continual improvement of emergency preparedness throughout the project lifecycle.

								
CHINA CIVIL ENGINEERING CONSTRUCTION CORPORATION–Dubai Branch R1181/2 Project Emergency Preparedness and Response Plan (PEPRP)		<table><tr><td>Doc. Ref:</td><td>CCECC-R1181/2-PEM-PLN-07</td></tr><tr><td>Rev. No.:</td><td>00</td></tr><tr><td>Date:</td><td>23 December 2025</td></tr></table>	Doc. Ref:	CCECC-R1181/2-PEM-PLN-07	Rev. No.:	00	Date:	23 December 2025
Doc. Ref:	CCECC-R1181/2-PEM-PLN-07							
Rev. No.:	00							
Date:	23 December 2025							

SECTION 8 – EMERGENCY RESPONSE PROCEDURES

This section outlines the tactical emergency response measures for all foreseeable emergency scenarios identified in the Project Risk Context


It includes ten (11) comprehensive procedures, including.

1. 8.1 FIRE & EXPLOSION EMERGENCY RESPONSE PROCEDURE (ERP-P01)
2. 8.2 EXCAVATION & TEMPORARY WORKS COLLAPSE RESPONSE PROCEDURE (ERP-P02)
3. 8.3 FALL FROM HEIGHT & SUSPENSION TRAUMA RESPONSE PROCEDURE (ERP-P03)
4. 8.4 UTILITY STRIKE RESPONSE PROCEDURE - (ERP-P04)
5. 8.5 TRAFFIC INCIDENT & PUBLIC SAFETY RESPONSE PROCEDURE (ERP-P05)
6. 8.6 MEDICAL EMERGENCY & HEAT STRESS RESPONSE PROCEDURE (ERP-P06)
7. 8.7 ENVIRONMENTAL SPILL RESPONSE PROCEDURE (ERP-P07)
8. 8.8 EXTREME WEATHER RESPONSE PROCEDURE (FLOOD / SANDSTORM) (ERP-P08)
9. 8.9 CONFINED SPACE RESCUE RESPONSE PROCEDURE (ERP-P09)
10. 8.10 MOBILE / CRAWLER CRANE EMERGENCY & RESCUE PROCEDURE (ERP-P10)
11. 8.11 PANDEMIC / INFECTIOUS DISEASE RESPONSE PROCEDURE (ERP- P11)

Each detailing the following components:

- Purpose
- Scope
- Activation triggers
- Roles and responsibilities
- Step-by-step response
- Communication plan
- Post-incident actions

The fully developed Emergency Response Procedures (ERP-P01 to ERP-P11) are presented in their complete form on the following page.

			
CHINA CIVIL ENGINEERING CONSTRUCTION CORPORATION–Dubai Branch R1181/2 Project Emergency Preparedness and Response Plan (PEPRP)		Doc. Ref:	CCECC-R1181/2-PEM-PLN-07
		Rev. No.:	00
		Date:	23 December 2025

8.1 FIRE & EXPLOSION (ERP-P01)

ERP-P01 – FIRE & EXPLOSION EMERGENCY RESPONSE PROCEDURE

Project: R1181/2 – Improvement of Al Safa Road

Document Ref: CCECC-R1181/2-ERP-P01

Linked Document: PROJECT EMERGENCY PREPAREDNESS AND RESPONSE PLAN (PEPRP)

1. PURPOSE

This procedure defines the immediate response actions, control measures, roles and responsibilities, required equipment, and training requirements for fire and explosion emergencies arising from construction activities, plant and machinery, fuel storage, hot works, temporary offices, and electrical systems. It aims to ensure prompt, coordinated action to control fires, protect personnel, and prevent escalation.

The objective is to **protect life, prevent fire spread or escalation, safeguard the public and assets**, and coordinate effectively with **Dubai Civil Defence**.

2. SCOPE

This ERP applies to:

- All project work areas, site offices, stores, and laydown yards
- Hot works, fuel storage, generators, and electrical installations
- Employees, subcontractors, visitors, and members of the public affected by project activities
- Day and night operations

This procedure shall be read in conjunction with:

- Hot Work Permit-to-Work
- Fire Risk Assessments and Method Statements
- UAE Fire & Life Safety Code of Practice
- Emergency Preparedness and Response Plan (EPRP)

3. TRIGGER / ACTIVATION CRITERIA

Activate this procedure immediately upon:

- Visible fire or smoke
- Explosion or suspected explosion risk
- Fuel, gas, or chemical ignition.
- Electrical fire or short circuit
- Activation of fire alarm or detection system

Incident Level: Level 1 to Level 4

(Level 4 where there is a major fire, explosion, fatality, or public impact)

4. KEY HAZARDS

- Rapid fire spread
- Explosion and blast effects
- Smoke inhalation
- Structural collapse due to fire
- Secondary incidents involving fuel, gas, or traffic.

5. ROLES & RESPONSIBILITIES

Sl. No..	ROLE	RESPONSIBILITIES
1.	Incident Commander	Overall command, authority liaison
2.	Emergency Coordinator	Activate ERT and emergency services
3.	Fire Wardens	Initial firefighting (if safe), evacuation
4.	Supervisors	Stop work, secure area
5.	First Aider / Nurse	Casualty care
6.	HSE Officer	Documentation and investigation support
7.	HSE Manager	Coordinate with Civil Defence
8.	TM Engineer	Control traffic

6. RESPONSE STRATEGY (ALARP PRINCIPLE)

- Life safety is the first priority.
- Attempt firefighting only if the fire is small and controllable.
- Evacuate immediately if fire escalates.
- Prevent spread by isolating fuel and power sources were safe.
- Do not re-enter affected areas until declared safe by authorities.

7. STEP-BY-STEP RESPONSE ACTIONS

7.1. Immediate Actions

- Shout “FIRE – FIRE – FIRE!”
- Stop all work.
- Activate nearest manual call point.
- Disconnect power supply.

7.2. Initial Firefighting (If Safe)

- Fire Wardens to use appropriate fire extinguishers.
- Only trained personnel to attempt firefighting.
- Maintain clear escape route at all times.

7.3. Evacuation & Scene Control

- Supervisors to ensure full evacuation to nearest muster point.
- Fire Wardens to check work areas and offices.
- Prevent unauthorised access to the fire zone.

7.4. Casualty Management

- First Aider to provide immediate care.
- Treat burns and smoke inhalation
- Arrange ambulance / hospital transfer as required.

8. FIREFIGHTING & RESCUE EQUIPMENT REQUIRED

- Fire extinguishers (CO₂, Dry Powder, Foam as applicable)
- Fire blankets
- Fire hose reels / hydrants (where provided)

- Rescue stretcher
- Oxygen cylinder
- AED
- First Aid Kit

All firefighting equipment shall be inspected, maintained, and accessible.

9. TRAINING & COMPETENCY REQUIREMENTS

Sl. No..	ROLE	RESPONSIBILITIES
1	Fire Wardens	Fire Warden & Extinguisher Training
2	Supervisors	Fire & Emergency Awareness
3	First Aiders	First Aid / BLS
4	Hot Work Operatives	Fire Safety Awareness
5	First Aider / Nurse	Casualty care
6	HSE Officer	Documentation and investigation support

10. COMMUNICATION & ESCALATION

- Follow escalation protocol as per EMP Section 4.7
- Dubai Civil Defence contacted immediately for uncontrolled fires.
- Client / Consultant notified through Incident Commander
- Power, fuel, and gas suppliers informed if affected.

11. POST-INCIDENT ACTIONS

- Secure and barricade affected area.
- Cool affected area, Ensure no re-ignition.
- Conduct headcount and confirm personnel safety.
- Incident investigation and reporting
- Review Fire Risk Assessment and Hot Work controls.
- Implement corrective and preventive actions.
- Submit incident report.
- Restore operations safely.

12. DRILLS & REVIEW

- Fire Drill: Monthly (or as required by authorities)
- Procedure reviewed after:
 - Drill outcomes
 - Actual fire incidents
 - Changes in site layout or fire risk

								
CHINA CIVIL ENGINEERING CONSTRUCTION CORPORATION—Dubai Branch R1181/2 Project Emergency Preparedness and Response Plan (PEPRP)		<table><tr><td>Doc. Ref:</td><td>CCECC-R1181/2-PEM-PLN-07</td></tr><tr><td>Rev. No.:</td><td>00</td></tr><tr><td>Date:</td><td>23 December 2025</td></tr></table>	Doc. Ref:	CCECC-R1181/2-PEM-PLN-07	Rev. No.:	00	Date:	23 December 2025
Doc. Ref:	CCECC-R1181/2-PEM-PLN-07							
Rev. No.:	00							
Date:	23 December 2025							

8.2 EXCAVATION & TEMPORARY WORKS COLLAPSE RESPONSE PROCEDURE (ERP-P02)

ERP-P02 –EXCAVATION & TEMPORARY WORKS COLLAPSE RESPONSE PROCEDURE

Project: R1181/2 – Improvement of Al Safa Road

Document Ref: CCECC-R1181/2-ERP-P02

Linked Document: PROJECT EMERGENCY PREPAREDNESS AND RESPONSE PLAN (PEPRP)

1. PURPOSE

This procedure defines the immediate response, rescue arrangements, roles, equipment, and training requirements for incidents involving collapse of excavations or temporary works, including trenches, pits, shoring systems, formwork, and support structures.

The objective is to protect life, prevent secondary collapse, and conduct safe rescue only by trained personnel.

2. SCOPE

This ERP applies to:

- All excavation activities (trenches, pits, shafts)
- Temporary work (shoring, formwork, support systems)
- Employees, subcontractors, and authorised visitors
- Day and night operations
- This procedure shall be read in conjunction with:
- Excavation / Temporary Works Permit-to-Work
- Approved Temporary Works Designs & Method Statements
- Project Emergency Preparedness and Response Plan (PEPRP)

3. TRIGGER / ACTIVATION CRITERIA

Activate this procedure immediately if:

- Partial or full collapse of an excavation occurs.
- Shoring or temporary support fails.
- A person is trapped, buried, or injured due to ground or structure failure.
- Incident Level: Level 2 to Level 4
(Level 4 where fatality, multiple casualties, or public impact exists)

4. KEY HAZARDS

- Secondary collapse
- Suffocation / asphyxiation
- Uncontrolled plant movement
- Falling materials
- Restricted access and visibility

5. ROLES & RESPONSIBILITIES

Sl. No..	ROLE	RESPONSIBILITIES
1	Incident Commander	Overall control and authority liaison
2	Emergency Coordinator	Activate ERT and emergency services
3	Rescue Team Lead	Control rescue operations
4	Site Supervisor	Stop work, secure area

Sl. No..	ROLE	RESPONSIBILITIES
5	First Aider / Nurse	Casualty care and stabilisation
6	HSE Officer	Documentation and investigation support
7	HSE Manager	Coordinate to Ambulance
8	TM Engineer	Control traffic

6. RESCUE STRATEGY (ALARP PRINCIPLE)

- Life safety is the priority.
- No mechanical pulling of casualties.
- No entry into unstable excavation
- Rescue actions must not create additional casualties.
- Emergency services to be involved without delay for serious incidents.

7. STEP-BY-STEP RESPONSE ACTIONS

7.1. Immediate Actions

- Stop all work immediately.
- Raise alarm and inform Emergency Coordinator
- Evacuate all personnel from the collapse zone.
- Isolate plants, machinery, and vibration sources

7.2. Scene Control

- Establish exclusion zone.
- Conduct headcount to identify missing persons.
- Assess ground stability from a safe distance.

7.3. Rescue Operations

- Where people are partially buried:
- Carefully clear soil by hand only
- Prioritise uncovering mouth and chest for breathing.
- Do NOT use excavators or plants for rescue!
- Await emergency services where collapse is extensive or unstable!

7.4. Casualty Management

- Once casualty is accessible:
- Apply first aid.
- Immobilise as required.
- Transfer using rescue stretcher.
- Arrange ambulance / hospital transfer as required.

8. RESCUE EQUIPMENT REQUIRED

- Hand digging tools (shovels)
- Rescue stretcher
- Spinal collar
- Oxygen cylinder
- AED
- First Aid Kit

- All equipment must be available, inspected, and serviceable prior to excavation works.

9. TRAINING & COMPETENCY REQUIREMENTS

SL. No..	ROLE	RESPONSIBILITIES
1	Rescue Team	Excavation Rescue Awareness
2	Supervisors	Excavation Safety & Emergency Response
3	First Aiders	First Aid / BLS
4	Temporary Works Supervisors	TW Awareness
5	Rescue Team	Excavation Rescue Awareness

10. COMMUNICATION & ESCALATION

- Follow escalation protocol as per EMP Section 4.7
- Emergency services contacted as required.
- Client / Consultant notified through Incident Commander

11. POST-INCIDENT ACTIONS

- Suspend all excavation / temporary work.
- Secure and barricade affected area.
- Conduct incident investigation.
- Review PTW, TW design, and inspection regime.
- Implement corrective and preventive actions.

12. DRILLS & REVIEW

- Excavation / Collapse Rescue Drill: Quarterly
- Procedure reviewed after:
 - Drill outcomes
 - Actual incidents
 - Change in excavation depth, method, or ground condition

8.3 FALL FROM HEIGHT & SUSPENSION TRAUMA RESPONSE PROCEDURE (ERP-P03)

ERP-P03 – FALL FROM HEIGHT & SUSPENSION TRAUMA RESPONSE PROCEDURE

Project: R1181/2 – Improvement of Al Safa Road

Document Ref: CCECC-R1181/2-ERP-P03

Linked Document: Project Emergency Preparedness and Response Plan (PEPRP)

1. PURPOSE

This procedure defines the immediate response, rescue arrangements, roles, equipment, and training requirements for incidents involving falls from height and suspension trauma arising from work on scaffolds, MEWPs, bridge edges, ramps, formwork, or elevated platforms.

The objective is to rescue the casualty without delay, prevent suspension trauma, and avoid secondary injuries.

2. SCOPE

This ERP applies to:

- All work at height activities
- MEWPs, scaffolding, bridge and ramp works
- Employees, subcontractors, and authorised visitors
- Day and night shifts
- This procedure shall be read in conjunction with:
- Work at Height Permit-to-Work
- Relevant Risk Assessments and Method Statements
- Emergency Preparedness and Response Plan (EPRP)

3. TRIGGER / ACTIVATION CRITERIA

Activate this procedure immediately if:

- A person falls from height.
- A person is suspended in a harness.
- A person is injured and cannot self-evacuate from height.
- Incident Level: Level 3 (may escalate to Level 4 if fatal or multiple casualties)

4. KEY HAZARDS

- Suspension trauma
- Internal injuries
- Head and spinal injuries
- Secondary falls during rescue
- Delayed rescue due to poor access

5. ROLES & RESPONSIBILITIES

Sl. No..	ROLE	RESPONSIBILITIES
1	Incident Commander	Overall control and escalation
2	Emergency Coordinator	Activate ERT and rescue resources
3	Height Rescue Team	Execute height rescue
4	First Aider / Nurse	Stabilise casualty
5	Supervisor	Secure area and stop work

Sl. No.,	ROLE	RESPONSIBILITIES
6	HSE Officer	Record incident and support investigation
7	HSE Manager	Coordinate with Paramedic Ambulance
8	TM Engineer	Control traffic

6. RESCUE STRATEGY (ALARP PRINCIPLE)

- Immediate rescue is critical to prevent suspension trauma.
- Use pre-planned rescue methods specific to the work location.
- Avoid improvisation and unsafe actions.
- Rescue must be performed only by trained personnel.

7. STEP-BY-STEP RESPONSE ACTIONS

7.1. Immediate Actions

- Stop working immediately.
- Raise alarm and inform Emergency Coordinator
- Secure the area below and around the casualty.

7.2. Rescue Operations

- Deploy height rescue equipment.
- Relieve load on suspended person immediately.
- Lower or retrieve casualty using approved rescue system.
- Do not leave a suspended person unattended.

7.3. Casualty Management

- Place casualty on rescue stretcher.
- Keep casualty in semi-sitting position initially.
- Provide first aid and oxygen.
- Arrange ambulance / hospital transfer as required.

8. RESCUE EQUIPMENT REQUIRED

- Height rescue kit (ropes, descenders)
- Rescue stretcher
- Harnesses and lifelines
- Oxygen cylinder
- AED
- First Aid Kit
- All equipment must be available, inspected, and ready prior to work at height.

9. TRAINING & COMPETENCY REQUIREMENTS

Sl. No.,	ROLE	RESPONSIBILITIES
1	Height Rescue Team	Work at Height Rescue
2	MEWP Operators	MEWP Operator Certification
3	First Aiders	First Aid / BLS
4	Supervisors	WAH & Emergency Awareness

10. COMMUNICATION & ESCALATION

- Follow communication and escalation protocol defined in EMP Section 4.7
- Emergency services contacted as required.
- Client / Consultant notified through Incident Commander

11. POST-INCIDENT ACTIONS

- Suspend work at height.
- Secure equipment and access points
- Conduct investigation.
- Review rescue effectiveness.
- Implement corrective and preventive actions.

12. DRILLS & REVIEW

- Height Rescue Drill: Bi-annual
- Procedure reviewed after:
- Drill results
- Actual incidents
- Change in work method or equipment

		
CHINA CIVIL ENGINEERING CONSTRUCTION CORPORATION—Dubai Branch R1181/2 Project Emergency Preparedness and Response Plan (PEPRP)	Doc. Ref: CCECC-R1181/2-PEM-PLN-07 Rev. No.: 00 Date: 23 December 2025	

8.4 UTILITY STRIKE RESPONSE PROCEDURE (ERP-P04)

ERP-P04 – UTILITY STRIKE RESPONSE PROCEDURE - (For Electricity, Water, Gas, Fibre Optic, Drainage, Chilled Water)

Project: R1181/2 – Improvement of Al Safa Road

Document Ref: CCECC-R1181/2-ERP-P04

Linked Document: Project Emergency Preparedness and Response Plan (PEPRP)

8.4.1 PURPOSE

This procedure defines the immediate response actions required when **underground or overhead utilities** are struck, damaged, exposed, or compromised during construction works, ensuring life safety, protection of public infrastructure, and rapid coordination with utility authorities.

8.4.2 SCOPE

This procedure applies to all works involving:

- Excavation (mechanical and manual)
- HDD (Horizontal Directional Drilling)
- Trench work for utilities
- Piling and deep foundation works.
- Road crossing works
- Temporary and permanent diversions

Covers utilities:

- DEWA LV / HV Cables (11kV, 33kV, 132kV)
- DEWA Water (Sweet / TSE)
- Gas Network
- Chilled Water
- Etisalat/DU Fibre Optic
- Stormwater / Drainage Network

8.4.3 ACTIVATION TRIGGERS

This ERP activates when ANY of the following occur:

- Contact with live electrical cables (sparks, explosion, flash)
- Water leakage, pressurised water jet, burst pipeline.
- Gas smell, hissing sound, gas detector alarm
- Fibre optic cable cut or exposed (service interruption)
- Chilled water pipe rupture (fog-like vapour release)
- Equipment strikes on drainage pipelines.
- Unexpected utility found during excavation
- Damaged duct bank or utility chamber

ANY utility strike is considered a Level 2 or Level 3 emergency depending on severity.

8.4.4 ROLES & RESPONSIBILITIES

Table 8.3A— Utility Strike Roles and Responsibilities

Sl. No..	ROLE	IMMEDIATE RESPONSIBILITIES
1	Person Discovering Strike	Stop work, alert others, report to supervisor
2	Supervisor / Foreman	Secure area, notify ERT & Utility Engineer
3	ERT Leader	Take command, assess risk, enforce evacuation
4	Utility Engineer	Identify utility type, inform relevant authority

Sl. No..	ROLE	IMMEDIATE RESPONSIBILITIES
5	HSE Manager	Notify EMT, Parsons, RTA
6	Incident Commander	Escalate emergency level, request external agencies
7	TM Engineer	Implement road closures/diversions if near traffic
8	Environmental Officer	Manage water/fuel spills (if applicable)
	Person Discovering Strike	Stop work, alert others, report to supervisor

8.4.5 STEP-BY-STEP - UTILITY STRIKE RESPONSE PROCEDURE

A. FIRST RESPONSE BY WITNESS

- Stop work immediately.
- Shout: “UTILITY STRIKE – STAND CLEAR!”
- Warn all workers to move away from excavation.
- Do NOT touch machinery or tools in contact with the utility.
- Notify supervisor and ERT.

B. SITE ISOLATION AND SAFETY CONTROL

- ERT Leader arrives and isolates the area:
 - Create 10–30 m exclusion zone.
 - Prevent ignition sources.
 - Prevent public/pedestrian access.
- Shut down plant only if safe (electrical strikes may energize equipment).
- Evacuate workers to safe distance.
- Ensure no one enters trench/excavation.

C. IDENTIFY TYPE OF UTILITY STRUCK

Table 8.3B — Hazard Identification by Utility Type

Sl. No..	UTILITY TYPE	INDICATION	RISK LEVEL
1	LV/HV Cable	Sparks, loud bang, smoke	Catastrophic
2	Gas Pipe	Smell, hissing sound, dead vegetation	Catastrophic
3	Water Pipe	Water leakage/jet, flooding	Major
4	Chilled Water	Cold vapour fog, water discharge	Major
5	Fibre Optic	No visible hazard	Medium (service disruption)
6	Drainage / Sewer	Smell, backflow, collapse	Medium

D. NOTIFICATION PROTOCOL

Table 8.3C — Notification Flow

Sl. No..	CONTACT	ACTION REQUIRED	TIMEFRAME
1	HSE Manager	Notify EMT	Immediately

Sl. No..	CONTACT	ACTION REQUIRED	TIMEFRAME
2	Incident Commander	Notify Utilities Authority (DEWA/GAS/DU/Etisalat/Empower)	Within 2 minutes
3	RTA Control Room	Inform of disruption	Within 5 minutes
4	Parsons	Notify Consultant	Immediately
5	Dubai Police & Civil Defence	For HV/Gas strikes	Immediate
6	TM Engineer	Implement emergency TTM	Immediate

All utility damage must be reported to the client (RTA) within 15 minutes.

E. UTILITY-SPECIFIC EMERGENCY RESPONSE ACTIONS

5. Electrical Cable Strike (LV/HV) – HIGH RISK

- ❖ Do NOT touch equipment in contact with cable.
- ❖ Maintain a 10 m exclusion zone for LV and 30 m for HV.
- ❖ Wait for DEWA team to isolate power.
- ❖ Treat any worker near equipment as a potential electrical shock victim.
- ❖ Prepare rescue only after DEWA declares area safe.

6. Gas Pipeline Strike – EXTREME RISK

- ❖ Evacuate area upwind.
- ❖ No smoking, sparks, vehicles, or phones within 50 m.
- ❖ Shut down engines and generators.
- ❖ Activate gas detectors.
- ❖ Call Civil Defence (997) immediately.
- ❖ Utility Engineer coordinates with gas provider.

7. Water Pipeline Damage

- ❖ Do NOT enter flooded excavation.
- ❖ Install barriers to prevent collapse.
- ❖ Use pumps only after confirmed safe.
- ❖ Notify DEWA Water Division.

8. Fibre Optic Cable Cut

- ❖ Stop work and protect exposed fibre.
- ❖ Notify Etisalat/Du immediately.
- ❖ Do not attempt repair (handled only by certified utility team).

9. Chilled Water Line Damage

- ❖ Treat vapour mist as hazard (poor visibility).
- ❖ Avoid exposure — risk of skin burns from cold water.
- ❖ Notify Empower (chilled water authority).

10. Drainage/Sewer Line Damage

- 1) Avoid contact with wastewater.
- 2) DM Drainage Department must be notified for repair.
- 3) Environmental team deploys spill response materials.

F. Traffic Management During Utility Strike

If strike occurs near live road:

- ❖ TM Team installs emergency lane closures

		
CHINA CIVIL ENGINEERING CONSTRUCTION CORPORATION–Dubai Branch R1181/2 Project Emergency Preparedness and Response Plan (PEPRP)	Doc. Ref: CCECC-R1181/2-PEM-PLN-07 Rev. No.: 00 Date: 23 December 2025	

- ❖ VMS boards display warnings
- ❖ Police requested for traffic diversion
- ❖ Barriers used to maintain public safety

G. post-incident actions

1. Confirm all workers safe and accounted for.
2. Utility authority inspects and repairs damaged asset.
3. Conduct post-incident inspection for ground stability.
4. HSE Manager initiates investigation within 24 hours.
5. Submit formal reports to:
 - RTA
 - Parsons
 - DEWA / GAS / Etisalat / Du / Empower / DM
 - CCECC Senior Management

Work may only resume after written closure approval from utility authority.

8.4.6 Required Utility Emergency Equipment

Table 8.3D — Utility Emergency Equipment

Sl. No..	EQUIPMENT	USE	RESPONSIBILITY
1	Gas detectors	Identify gas leaks	Utility Engineer
2	Barricades & cones	Exclusion zone	TM Engineer
3	Spill kits	For water/sewer spills	Environmental Officer
4	Thermal camera	Detect overheated electrical components	HSE
5	PPE (insulated gloves, arc flash gear)	Electrical safety	ERT
6	Pumps	Flood water removal	Construction Manager

								
CHINA CIVIL ENGINEERING CONSTRUCTION CORPORATION–Dubai Branch R1181/2 Project Emergency Preparedness and Response Plan (PEPRP)		<table><tr><td>Doc. Ref:</td><td>CCECC-R1181/2-PEM-PLN-07</td></tr><tr><td>Rev. No.:</td><td>00</td></tr><tr><td>Date:</td><td>23 December 2025</td></tr></table>	Doc. Ref:	CCECC-R1181/2-PEM-PLN-07	Rev. No.:	00	Date:	23 December 2025
Doc. Ref:	CCECC-R1181/2-PEM-PLN-07							
Rev. No.:	00							
Date:	23 December 2025							

8.5 TRAFFIC INCIDENT & PUBLIC SAFETY RESPONSE PROCEDURE (ERP-P05)

ERP-P05 – TRAFFIC INCIDENT & PUBLIC SAFETY RESPONSE PROCEDURE

Project: R1181/2 – Improvement of Al Safa Road

Document Ref: CCECC-R1181/2-ERP-P05

Linked Document: Project Emergency Preparedness and Response Plan (PEPRP)

8.5.1. PURPOSE

To define the actions required to protect life, secure the site, prevent secondary accidents, restore safe traffic flow, and coordinate with Dubai Police and RTA during any traffic-related emergency within or near the work zones of Project R1181/2.

8.5.2. SCOPE

This ERP applies to:

- All temporary traffic management (TTM) zones
- Project vehicles, plant, and public road users
- Inside construction work zones
- Day and night operations
- Plant crossing locations.
- Areas with pedestrian access
- Heavy machinery movement zones
- This procedure shall be read in conjunction with:
- Approved Traffic Management Plans (TMPs)
- RTA Work Zone Traffic Management Manual
- Relevant Method Statements
- Project Emergency / Contingency and Business Continuity Plan

8.5.3. TRIGGER / ACTIVATION CRITERIA

This ERP is activated when any of the following occur:

- Public vehicle collision near or inside work zone
- Worker struck by vehicle or plant.
- Plant-to-vehicle impact.
- Pedestrian hit by vehicle
- Loss or failure of traffic control devices (VMS, barriers, cones)
- Public intrusion into restricted areas
- Road flooding or obstruction causing traffic hazard.

8.5.4. KEY HAZARDS

- Secondary traffic collisions
- Pedestrian intrusion into work zones
- Fire, fuel leakage, or vehicle instability.
- Limited visibility (night works / adverse weather)
- Public safety exposure

8.5.5. ROLES & RESPONSIBILITIES

Sl. No..	ROLE	IMMEDIATE RESPONSIBILITIES
1	Person Reporting Incident	Call ERT & Supervisor, warn area workers

SL. No..	ROLE	IMMEDIATE RESPONSIBILITIES
2	ERT Leader	Take command, assess hazard, secure the scene
3	Traffic Management Engineer	Deploy emergency diversion plan
4	TM Supervisors	Set up cones, barriers, VMS messages
5	First Aid Team / Site Nurse	Administer first aid, coordinate ambulance
6	HSE Manager	Notify EMT, RTA, Parsons
7	Incident Commander	Escalates to Dubai Police and Civil Defence if required
8	Dubai Police	Lead investigation for vehicle collisions
9	RTA Control Room	Activate external diversion, public alerts

8.5.6. RESPONSE STRATEGY (ALARP PRINCIPLE)

- Life safety and public protection are the first priority.
- Immediate traffic control to prevent secondary incidents.
- Do not move vehicles unless required to save life or instructed by authorities.
- Coordinate closely with Dubai Police and RTA

8.5.7. STEP-BY-STEP TRAFFIC INCIDENT RESPONSE PROCEDURE ACTION

A. Immediate Actions by Witness


1. Shout: "TRAFFIC INCIDENT — STOP WORK!"
2. Move workers away from the road toward safe zones.
3. Notify Supervisor and ERT.
4. Do NOT move injured persons unless necessary for safety.

B. ERT Arrival & Scene Stabilisation

1. ERT Leader assumes control.
2. Identify hazards:
 - Oncoming traffic
 - Fuel leakage
 - Fire risk
 - Unstable vehicles
3. Stop all nearby machinery.
4. Secure the accident area using:
 - Cones
 - Barriers
 - Warning lamps
 - Flagmen

C. Traffic Management Team Actions

1. TM Engineer activates **Emergency Diversion Plan**.
2. TM Supervisors deploy:
 - Taper closures
 - Buffer zones
 - Arrow boards
 - VMS emergency messages ("ACCIDENT AHEAD – USE CAUTION")

								
CHINA CIVIL ENGINEERING CONSTRUCTION CORPORATION–Dubai Branch R1181/2 Project Emergency Preparedness and Response Plan (PEPRP)		<table><tr><td>Doc. Ref:</td><td>CCECC-R1181/2-PEM-PLN-07</td></tr><tr><td>Rev. No.:</td><td>00</td></tr><tr><td>Date:</td><td>23 December 2025</td></tr></table>	Doc. Ref:	CCECC-R1181/2-PEM-PLN-07	Rev. No.:	00	Date:	23 December 2025
Doc. Ref:	CCECC-R1181/2-PEM-PLN-07							
Rev. No.:	00							
Date:	23 December 2025							

3. Arrange Police access lane.
4. Prevent public entry into the work site.

D. Injury Management & Evacuation

1. First Aider/Nurse assesses injured persons.
2. Call 998 Ambulance for serious injuries.
3. For minor injuries:
 - Provide first aid.
 - Transfer to clinic if safe
4. For unconscious or trapped victims:
 - Notify Civil Defence (if entrapment)
 - Do NOT move victim unless directed by medical experts.
5. Secure injured area until police arrive.

E. Fire / Fuel Leak Control

If fuel or oil spill observed:

- HSE Officer and Logistic team with deploys spill kits.
- ERT removes ignition sources.
- Fire Wardens keep extinguishers ready.

If fire risk is high → immediately call **997 (Civil Defence)**.

F. Notification Protocol

Table 8.4B — Notification Flow

Sl. No.,	WHO	NOTIFIED BY	TIMEFRAME
1	Dubai Police (999)	Incident Commander	Immediately for any vehicle collision
2	Ambulance (998)	First Aider	Immediately if injured
3	RTA Control Room	HSE Manager	Within 5 min
4	Parsons Consultant	HSE Manager	Immediately
5	Project Director	HSE Manager	Immediately
6	Traffic Diversion Teams	TM Engineer	Immediately

Police take legal control of accident scene involving public.

G. Public Safety & Incident Perimeter Control

1. Establish minimum 50 m safety perimeter.
2. Deploy flagmen to slow oncoming traffic.
3. Ensure nighttime visibility with flashing beacons and flood lights.
4. Redirect public vehicles to alternate routes.

H. Recovery / Clearance Operations

Only after Dubai Police gives permission:

1. Remove damaged vehicles from work zone.
2. Clear debris, damaged cones, barriers.

		
CHINA CIVIL ENGINEERING CONSTRUCTION CORPORATION–Dubai Branch R1181/2 Project Emergency Preparedness and Response Plan (PEPRP)		Doc. Ref: CCECC-R1181/2-PEM-PLN-07 Rev. No.: 00 Date: 23 December 2025

3. Reinstate the Traffic Management Plan.
4. Inspect crash barriers and road surfaces.
5. Reopen lanes gradually under TM Engineer supervision.

No work allowed to resume until TM Engineer and HSE Manager sign off.

I. Post-Incident Actions

1. Confirm all personnel are accounted for.
2. Document:
 - Photographs
 - VMS messages used
 - Traffic position
 - Witness statements
3. Complete Incident Report within 24 hours.
4. Submit to:
 - RTA
 - Parsons
 - Dubai Police (if required)
 - CCECC Senior Management

8.5.8. Equipment Required for Traffic Incident Response

Table 8.4C — Emergency Traffic Equipment

Sl. No.,	WHO	NOTIFIED BY	TIMEFRAME
1	Cones / Barriers	Road closure & traffic diversion	TM Supervisor
2	VMS Boards	Warn motorists	TM Engineer
3	Reflective Flags	Control traffic manually	Flagmen
4	Spill Kits	Fuel/oil spill cleanup	Environmental Officer
5	First Aid Kits	Injury management	Site Nurse
6	Fire Extinguishers	Vehicle fire suppression	Fire Wardens
7	Warning Lamps	Night visibility	TM Crew
8	Radios	Communication	ERT / TM Team

8.5.9. COMMUNICATION & ESCALATION

1. Follow escalation protocol as per EMP Section 4.7
2. Emergency services contacted as required
3. RTA Control Room and Police coordinated through Incident Commander
4. Client / Consultant notified by Project Director

8.5.10. POST-INCIDENT ACTIONS

1. Restore traffic only after authority clearance

								
CHINA CIVIL ENGINEERING CONSTRUCTION CORPORATION–Dubai Branch R1181/2 Project Emergency Preparedness and Response Plan (PEPRP)		<table><tr><td>Doc. Ref:</td><td>CCECC-R1181/2-PEM-PLN-07</td></tr><tr><td>Rev. No.:</td><td>00</td></tr><tr><td>Date:</td><td>23 December 2025</td></tr></table>	Doc. Ref:	CCECC-R1181/2-PEM-PLN-07	Rev. No.:	00	Date:	23 December 2025
Doc. Ref:	CCECC-R1181/2-PEM-PLN-07							
Rev. No.:	00							
Date:	23 December 2025							

2. Secure and document the scene
3. Conduct incident investigation
4. Review TMP effectiveness and controls
5. Implement corrective and preventive actions

8.5.11. DRILLS & REVIEW

1. Traffic Incident Drill: Quarterly
2. Procedure reviewed after:
3. Drill outcomes
4. Actual incidents
5. TMP or staging changes

			
CHINA CIVIL ENGINEERING CONSTRUCTION CORPORATION—Dubai Branch R1181/2 Project Emergency Preparedness and Response Plan (PEPRP)		Doc. Ref:	CCECC-R1181/2-PEM-PLN-07
		Rev. No.:	00
		Date:	23 December 2025

8.6 MEDICAL EMERGENCY & HEAT STRESS RESPONSE PROCEDURE (ERP-P06)

ERP-P06 – MEDICAL EMERGENCY & HEAT STRESS RESPONSE PROCEDURE

Project: R1181/2 – Improvement of Al Safa Road

Document Ref: CCECC-R1181/2-ERP-P06

Linked Document: Project Emergency Preparedness and Response Plan (PEPRP)

8.6.1. PURPOSE

This procedure defines the immediate response, roles, equipment, and training requirements for medical emergencies, including heat stress, heat exhaustion, heat stroke, sudden illness, collapse, and traumatic injury occurring on the project.

The objective is to stabilise the casualty quickly, prevent deterioration, and ensure timely medical evacuation.

8.6.2. SCOPE

This ERP applies to:

- All project work areas, offices, and welfare facilities
- Employees, subcontractors, visitors, and authorised personnel
- Day and night operations, including summer peak conditions.
- This procedure shall be read in conjunction with:
- Project Heat Stress Management Plan
- First Aid Arrangements
- Project Emergency / Contingency and Business Continuity Plan
- Project Emergency Preparedness and Response Plan (PEPRP)

8.6.3. TRIGGER / ACTIVATION CRITERIA

Activate this procedure immediately upon:

- Collapse, loss of consciousness, or severe illness.
- Suspected heat exhaustion or heat stroke
- Serious injury requiring medical attention.
- Any medical condition where self-recovery is not possible.
- Incident Level: Level 1 to Level 4
(Level 4 where fatality or multiple casualties occur)

8.6.4. KEY HAZARDS

- Heat stroke and dehydration.
- Cardiac or respiratory distress
- Secondary injury due to delayed response
- Exposure to sun and high humidity

8.6.5. ROLES & RESPONSIBILITIES

8.6 A — Medical Emergency Responsibilities

Sl. No..	ROLE	IMMEDIATE RESPONSIBILITIES
1	Person Discovering Victim	Call for help, alert supervisor/ERT

Sl. No..	ROLE	IMMEDIATE RESPONSIBILITIES
2	First Aider	Assess patient, provide first aid
3	Site Nurse / Medical Team	Lead medical response, triage, stabilize
4	ERT Leader	Secure area, coordinate rescue
5	Supervisor	Prevent re-entry, support medical evacuation
6	HSE Manager	Notify EMT, RTA, Parsons
7	Incident Commander	Decide escalation, request ambulance
8	Ambulance (998)	Provide advanced medical care & transport

8.6.6. RESPONSE STRATEGY (ALARP PRINCIPLE)

- Life safety is the priority.
- Provide immediate first aid.
- Reduce heat exposure and stabilise casualty.
- Do not delay medical evacuation where symptoms are severe.

8.6.7. STEP-BY-STEP MEDICAL EMERGENCY RESPONSE PROCEDURE

A. Immediate Actions by Witness

1. Call out: "MEDICAL EMERGENCY – CALL FIRST AID!"
2. Ensure scene is safe (no falling materials, traffic, electrical hazards).
3. Do NOT move the victim unless in danger.
4. Notify First Aider / Supervisor.

B. First Aid Team Assessment

1. First Aider approaches with PPE.
2. Perform Primary Assessment (DR-ABC):
 - D – Danger
 - R – Response (Are they conscious?)
 - A – Airway
 - B – Breathing
 - C – Circulation
3. If no breathing or pulse → Start CPR immediately.
4. Use AED if cardiac arrest suspected.
5. Treat visible injuries:
 - Bleeding → apply pressure.
 - Burn → remove heat source, cool burn.
 - Fracture → immobilize.

C. Heat Stress / Heat Stroke Response

1. Move patient to shaded, cool area.
2. Remove PPE, loosen clothing.
3. Apply cool water, fans, ice packs to armpits/groin.
4. Provide electrolyte drinks (if conscious).
5. Monitor vital signs.
6. If unconscious or seizures occur → call 998 immediately.

								
CHINA CIVIL ENGINEERING CONSTRUCTION CORPORATION–Dubai Branch R1181/2 Project Emergency Preparedness and Response Plan (PEPRP)		<table><tr><td>Doc. Ref:</td><td>CCECC-R1181/2-PEM-PLN-07</td></tr><tr><td>Rev. No.:</td><td>00</td></tr><tr><td>Date:</td><td>23 December 2025</td></tr></table>	Doc. Ref:	CCECC-R1181/2-PEM-PLN-07	Rev. No.:	00	Date:	23 December 2025
Doc. Ref:	CCECC-R1181/2-PEM-PLN-07							
Rev. No.:	00							
Date:	23 December 2025							

D. Calling Emergency Services (Ambulance 998)

Call 998 if:

- Victim is unconscious.
- Breathing is irregular or absent.
- Severe bleeding
- Possible head, neck, or spine injury
- Seizure, heart attack symptoms
- Heat stroke (core temperature > 40°C)
- Multiple casualties

Provide:

- Site location
- Type of injury
- Number of victims
- Access route

ERT escorts ambulance to location.

E. Area Control & Safety

1. ERT Leader sets a safety perimeter around patient.
2. Stop nearby operations.
3. TM Engineer diverts traffic if incident occurred near road.
4. Prevent crowding at the scene.

F. Patient Transfer & Handover

1. Upon ambulance arrival, First Aider briefs paramedics.
2. Provide:
 - Vital signs
 - Treatment applied
 - Medical history (if known)
3. Assist with stretcher transfer if requested.

G. After-Action Requirements

1. Secure incident area.
2. Incident investigation starts within 24 hours.
3. Complete:
 - Medical Incident Form
 - Heat Stress Report (if applicable)
4. Submit report to:
 - RTA
 - Parsons
 - CCECC Management
5. Review for:
 - PPE compliance
 - Heat stress prevention improvements.
 - Work-rest cycle effectiveness.

8.6.8. REQUIRED MEDICAL & HEAT RESPONSE EQUIPMENT

Table 8.5B — Equipment Required

Sl. No..	EQUIPMENT	USE	LOCATION
1	First Aid Kits	Immediate treatment	All work zones & vehicles
2	AED (Defibrillator)	Cardiac arrest	Site office / Medical room
3	Trauma Kits	Severe injuries	ERT Vehicle
4	Ice boxes / Ice packs	Heat stress management	All active zones
5	Oxygen kit	Respiratory issues	Medical room
6	Stretcher	Casualty transport	ERT
7	Hydration stations	Heat illness prevention	Multiple zones
8	Wheelchair	Transport of conscious patient	Medical room

8.6.9. COMMUNICATION & ESCALATION

1. Follow escalation protocol as per EMP Section 4.7
2. Emergency services contacted as required
3. Client / Consultant notified through Incident Commander

8.6.10. POST-INCIDENT ACTIONS

1. Record incident details
2. Review work/rest regime and heat controls
3. Investigate root cause
4. Implement corrective and preventive actions

8.6.11. DRILLS & REVIEW

1. Medical / Heat Stress Drill: Quarterly (summer focused)
2. Procedure reviewed after:
3. Drill outcomes
4. Actual incidents
5. Seasonal changes

			
CHINA CIVIL ENGINEERING CONSTRUCTION CORPORATION—Dubai Branch R1181/2 Project Emergency Preparedness and Response Plan (PEPRP)		Doc. Ref:	CCECC-R1181/2-PEM-PLN-07
		Rev. No.:	00
		Date:	23 December 2025

8.7 ENVIRONMENTAL SPILL RESPONSE PROCEDURE (ERP-P07)

ERP-P07– ENVIRONMENTAL SPILL RESPONSE PROCEDURE

Project: R1181/2 – Improvement of Al Safa Road

Document Ref: CCECC-R1181/2-ERP-P07

Linked Document: Project Emergency Preparedness and Response Plan (PEPRP)

8.7.1. PURPOSE

To define the required steps to safely contain, control, and clean up any spill of hazardous or non-hazardous materials to prevent harm to personnel, property, soil, stormwater drains, and the environment.

8.7.2. SCOPE

This procedure applies to all:

- Fuel dispensing & refuelling areas.
- Plant yard & vehicle maintenance zones.
- Bitumen and chemical storage
- Construction and utility work fronts
- Concrete washout operations
- Any location where hazardous substances are stored, handled, or transported.

Covers spills of:

- Diesel
- Hydraulic oil
- Engine oil
- Chemicals, paints, solvents
- Bitumen / emulsion
- Concrete slurry / washout
- Sewage leakage from tanker or drainage line
- Any unknown liquid

8.7.3. ACTIVATION TRIGGERS

This ERP activates when:

- Any liquid substance is spilled onto ground or paved surfaces.
- Fuel, oil or chemicals leak from equipment or tankers.
- Concrete washout enters stormwater drain.
- Hazardous vapors detected
- Spill impacts public road or water channels.
- Any quantity large enough to pose environmental, fire, or safety risk.

8.7.4. ROLES & RESPONSIBILITIES

Table 8.6A – Spill Response Responsibilities

Sl. No..	ROLE	IMMEDIATE RESPONSIBILITIES
1	Person Discovering Spill	Stop work, alert others, notify Supervisor/ERT
2	Supervisor	Secure area, prevent spread, call Environmental Officer
3	ERT Leader	Take control, assess risk, declare spill category (minor/major)
4	Environmental Officer	Lead containment, coordinate disposal

Sl. No..	ROLE	IMMEDIATE RESPONSIBILITIES
5	Fire Wardens	Assist if spill is flammable
6	TM Engineer	Close lanes if spill affects public road
7	HSE Manager	Notify EMT, RTA/Parsons if required
8	Incident Commander	Escalate to DM or Civil Defence if needed

8.7.5. SPILL CLASSIFICATION

8.6B – Spill Severity Categories

Sl. No..	CATEGORY	DESCRIPTION	RESPONSE LEVEL
1	Minor Spill (< 20 liters)	Small diesel/oil leak; easily contained	ERT + logistic + HSE Team
2	Moderate Spill (20–200 liters)	Requires multiple spill kits, affects work area	ERT + logistic + HSE Team
3	Major Spill (> 200 liters)	Affects road, drainage, public area; explosive/chemical spill	Incident Commander + DM + Civil Defence

Major spills require Dubai Municipality to be notified.

8.7.6. STEP-BY-STEP SPILL RESPONSE PROCEDURE

A. Immediate Actions by Witness

1. Shout: “SPILL – STOP WORK!”
2. Stop the source (close valve, stop engine) if safe to do so.
3. Prevent workers from walking through contaminated area.
4. Notify Supervisor and ERT.

B. B. ERT ARRIVAL & HAZARD ASSESSMENT

ERT Leader evaluates:

1. Type of liquid (fuel, chemical, oil, sewage, bitumen)
2. Quantity and spread
3. Fire/explosion risk
4. Drainage contamination risk
5. Environmental impact

If flammable → remove ignition sources.

C. CONTAINMENT ACTIONS

1. Deploy spill kits immediately.
2. Construct containment barriers using:
 - Absorbent pads
 - Booms
 - Soil/sand berms

		
CHINA CIVIL ENGINEERING CONSTRUCTION CORPORATION–Dubai Branch R1181/2 Project Emergency Preparedness and Response Plan (PEPRP)		Doc. Ref: CCECC-R1181/2-PEM-PLN-07 Rev. No.: 00 Date: 23 December 2025

3. Prevent spill from entering:
 - Stormwater drains
 - Excavations
 - Public road lanes
4. Shut down equipment in affected area.

D. CLEAN-UP & RECOVERY

1. Use absorbent materials to soak up liquid.
2. Collect contaminated pads/soil into hazardous waste bags.
3. For concrete spills:
 - Contain slurry.
 - Remove with vacuum or absorbents.
4. For bitumen spills:
 - Allow to cool.
 - Remove manually with scrapers.
5. Store waste in DM-approved waste containers.

E. DISPOSAL

Logistic and HSE Officer arranges disposal through **DM-approved waste contractor**.

Waste types:

- **Hazardous Waste:** oil, contaminated soil, paint, solvents
- **Non-hazardous Waste:** small debris, sand used for containment.

Disposal records are maintained in the Environmental Logbook.

F. Notifications

Table 8.6C — Notification Flow

Sl. No..	WHO	NOTIFIED BY	TIMEFRAME
1	Minor Spill	HSE Officer	Within 30 min
2	Moderate Spill	HSE Manager / Parsons	Within 15 min
3	Major Spill	Dubai Municipality 800900 / RTA	Immediately

A spill entering drainage or public roads is automatically Major.

G. Road Traffic Safety (If spill affects carriageway)

TM Engineer must:

1. Deploy emergency TTM diversion
2. Install warning “SLIPPERY ROAD” signage
3. Clean and dry road surface before reopening
4. Inspect skid resistance

No road is reopened until approved by HSE + TM Engineer.

H. Post-Spill Actions

1. HSE Officer inspects area for residual contamination.
2. Conduct soil sampling if required.

3. Refill spill kit stations.
4. HSE conducts investigation within 24 hours.
5. Lessons learned communicated via toolbox talks.

8.7.7. Required Spill Response Equipment

8.6D – Spill Control Equipment

Sl. No.,	Equipment	Use	Location
1	Spill kits (oil/chemical)	Containment, absorption	Fuel storage, plant yard, work fronts
2	Absorbent booms	Prevent spread of liquid	Spill stations
3	Drain covers	Protect stormwater access	TM Stores
4	Shovels/scrapers	Remove contaminated soil	ERT vehicle
5	Hazardous waste bags	Waste collection	Environmental office
6	Sandbags	Quick containment	Yard
7	Fire extinguisher	For flammable spills	Hot work & fuelling areas

8.7.8. COMMUNICATION & ESCALATION

1. Follow escalation protocol as per EMP Section 4.7
2. Inform Dubai Municipality and RTA where required
3. Emergency services contacted if fire or health risk exists
4. Client / Consultant notified through Incident Commander

8.7.9. POST-INCIDENT ACTIONS

1. Secure affected area
2. Record and investigate incident
3. Review storage, handling, and refuelling procedures
4. Implement corrective and preventive actions
5. Update environmental risk assessments if required

8.7.10. DRILLS & REVIEW

1. Spill Response Drill: Bi-annual
2. Procedure reviewed after:
3. Drill outcomes
4. Actual spill incidents
5. Change in materials or site conditions

								
CHINA CIVIL ENGINEERING CONSTRUCTION CORPORATION–Dubai Branch R1181/2 Project Emergency Preparedness and Response Plan (PEPRP)		<table><tr><td>Doc. Ref:</td><td>CCECC-R1181/2-PEM-PLN-07</td></tr><tr><td>Rev. No.:</td><td>00</td></tr><tr><td>Date:</td><td>23 December 2025</td></tr></table>	Doc. Ref:	CCECC-R1181/2-PEM-PLN-07	Rev. No.:	00	Date:	23 December 2025
Doc. Ref:	CCECC-R1181/2-PEM-PLN-07							
Rev. No.:	00							
Date:	23 December 2025							

8.8 ERP-P08 – EXTREME WEATHER RESPONSE PROCEDURE (FLOOD / SANDSTORM)

ERP-P08 – EXTREME WEATHER RESPONSE PROCEDURE (FLOOD / SANDSTORM)

Project: R1181/2 – Improvement of Al Safa Road

Document Ref: CCECC-R1181/2-ERP-P09

Linked Document: Project Emergency Preparedness and Response Plan (PEPRP)

8.8.1. PURPOSE

This procedure defines the preparedness and response actions, roles, equipment, and escalation measures for extreme weather events, including heavy rain, flash flooding, sandstorms, and reduced visibility, that may affect personnel safety, traffic operations, excavations, and temporary works.

The objective is to protect life, secure the site, prevent secondary incidents, and enable safe resumption of works once conditions stabilize.

8.8.2. SCOPE

Applies to all project locations including:

- Open excavations
- Bridge works, ramps, scaffoldings
- Crane operations & lifting activities.
- Traffic diversions
- Utility trenches & HDD pits
- Stockyard and material storage

8.8.3. EXTREME WEATHER TYPES COVERED

- Heavy rainfall
- Flash flooding
- Sandstorm / dust storm
- High winds
- Lightning storms
- Low-visibility conditions (<50 m)

8.8.4. ACTIVATION TRIGGERS

ERP-P08 activates when:

- Weather alerts issued by NCMS / RTA / Site HSE
- Visibility below safe limits
- Floodwater entering excavations.
- Winds > 25 km/h (suspend lifting operations)
- Lightning within 10 km radius
- Severe rainfall affecting work zones.

8.8.5. KEY HAZARD

- Flooding of excavations and confined spaces
- Reduced visibility leading to traffic or plant incidents.
- Collapse of temporary works due to water ingress
- Flying debris during high winds
- Electrical hazards due to water exposure

8.8.6. ROLES & RESPONSIBILITIES

8.7A – Extreme Weather Responsibilities

Sl. No..	ROLE	IMMEDIATE RESPONSIBILITIES
1	HSE Manager	Issue weather alert to all teams
2	ERT Leader	Evacuate workers from exposed zones
3	Construction Manager	Secure excavations, work area, materials and plant
4	TM Engineer	Adjust / divert traffic as needed and Implement emergency TMP adjustments
5	HSE Officer	Monitor flooding & site drainage
6	Crane/Lifting Supervisor	Stop all lifting during high winds
7	Site Engineers	Secure equipment and power sources
8	Supervisors	Stop work and evacuate affected areas

8.8.7. RESPONSE STRATEGY (ALARP PRINCIPLE)

- Early decision-making based on forecasts
- Stop work before conditions become unsafe.
- Protect excavations and traffic interfaces.
- Prioritise personnel safety over productivity.
- Resume works only after formal safety clearance.

8.8.8. STEP-BY-STEP EXTREME WEATHER RESPONSE

A. Weather Alert Received

1. HSE sends SMS / WhatsApp / Radio Broadcast to all teams.
2. All high-risk activities stop immediately:
 - Lifting
 - Working at height
 - Hot works
 - Excavation entry

B. Heavy Rain / Flood Response

1. Evacuate workers from:
 - Excavations
 - HDD pits
 - Shafts
 - Tunnels
2. Activate dewatering pumps.
3. Install sandbags around pit edges.
4. Disconnect power tools from wet zones.
5. TM Engineer:
 - Close affected traffic lanes
 - Install "FLOODING AHEAD" signage.

- Environmental team monitors water levels every 10 minutes.

C. Sandstorm / Dust Storm Response

- Stop work immediately if visibility < 50 m.
- Evacuate workers to sheltered areas.
 - Secure loose materials:
 - Cones
 - Barriers
 - Formwork
 - Timber
- Workers must not walk near live traffic sections.
- TM Engineer deploys:
 - Flashing beacons
 - Warning boards
 - Reduced speed signage

D. High Wind Response

Actions required at wind speeds:

Sl. No.,	WIND SPEED	ACTION
1	>20 km/h	Monitor cranes and scaffolding
2	>25 km/h	Stop lifting operations
3	>30 km/h	Evacuate scaffold & MEWP operations
4	>40 km/h	Stop ALL external work

Secure:

- Cranes (slew free)
- MEWPs lowered
- Temporary structures reinforced

E. Lightning Response

- Stop all outdoor work.
- Evacuate workers from:
 - Scaffolds
 - Metal structures
 - Crane cabins
 - Open fields
- Maintain 10 km lightning safety radius.
- Resume work only after 30 min with no strikes.

F. Post-Weather Inspection

- Inspect:
 - Excavation stability

- Electrical systems
 - Scaffolding
 - Cranes & MEWPs
 - Traffic management devices
2. Record findings & corrective actions.
 3. HSE authorizes work resumption.

8.8.9. COMMUNICATION & ESCALATION

- Follow escalation protocol as per EMP Section 4.7
- RTA Control Room informed for major traffic impact.
- Emergency services contacted if life safety is threatened.
- Client / Consultant notified through Incident Commander

POST-EVENT ACTIONS

- Inspect excavations, temporary works, and traffic arrangements.
- Verify ground stability and drainage.
- Remove accumulated water and debris.
- Conduct safety clearance before resuming works!
- Record event and lessons learned.

8.8.10. DRILLS & REVIEW

- Extreme Weather Drill: Annual (pre-rainy season)
- Procedure reviewed after:
- Actual weather events
- Drill outcomes
- Changes in site conditions or staging

8.9 ERP- CONFINED SPACE RESCUE RESPONSE PROCEDURE

ERP-P9 – CONFINED SPACE RESCUE RESPONSE PROCEDURE

Project: R1181/2 – Improvement of Al Safa Road

Document Ref: CCECC-R1181/2-ERP-P9

Linked Document: Project Emergency Preparedness and Response Plan (PEPRP)

8.9.1. PURPOSE

This Emergency Response Procedure (ERP-P10) defines the planned response, rescue arrangements, roles, equipment, and training requirements for any confined space emergency arising on Project R1181/2, including manholes, chambers, culverts, ducts, and utility pits.

The procedure ensures that rescue from confined space is conducted safely, systematically, and only by trained personnel, to prevent secondary casualties.

8.9.2. SCOPE

This procedure applies to all:

- Confined space activities on the project
- Employees, subcontractors, and authorised visitors
- Planned and unplanned confined space entries
- Day and night operations
- This ERP shall be read in conjunction with:
- Confined Space Entry Permit-to-Work
- Project Risk Assessments and Method Statements
- Emergency Preparedness and Response Plan (EPRP)

8.9.3. TRIGGER / ACTIVATION CRITERIA

This procedure shall be activated immediately upon occurrence of any of the following:

- Injury or collapse of a person inside a confined space
- Loss of consciousness or suspected oxygen deficiency
- Toxic or flammable gas alarm activation
- Sudden water ingress or flooding
- Any situation where normal self-evacuation is not possible.
- Incident Level: Level 2 to Level 4 (as per EMP escalation matrix)

8.9.4. KEY HAZARDS

- Oxygen deficiency / toxic atmosphere
- Restricted access and egress
- Risk of secondary casualties
- Engulfment, flooding, or collapse
- Delayed rescue due to poor access

8.9.5. ROLES & RESPONSIBILITIES

Sl. No..	ROLE	IMMEDIATE RESPONSIBILITIES
1	Incident Commander	Overall control, authority liaison
2	Emergency Coordinator	Activate ERT, coordinate rescue

Sl. No..	ROLE	IMMEDIATE RESPONSIBILITIES
3	CSE Supervisor	Control entry, ensure permit compliance
4	Confined Space Rescue Team	Execute rescue operations
5	Standby Person	Monitor entry, raise alarm
6	First Aider / Nurse	Casualty care and stabilization
7	HSE Officer	Documentation, investigation support

8.9.6. RESCUE STRATEGY (ALARP PRINCIPLE)

The project adopts a NON-ENTRY RESCUE FIRST philosophy.

- Rescue hierarchy:
- Non-entry rescue using winch / tripod.
- Assisted rescue from outside the space.
- Entry rescue only when:
- Atmosphere is tested and acceptable, or
- BA and trained personnel are available.

⚠ Untrained personnel shall NEVER enter a confined space to attempt rescue.

8.9.7. STEP-BY-STEP RESPONSE ACTIONS

8.9.7.1. Immediate Actions

- Stop work at once.
- Raise alarm and inform Emergency Coordinator
- Prohibit further entry into confined space.
- Initiate emergency response

8.9.7.2. Atmosphere Assessment

- Evaluate atmosphere using calibrated gas monitor.
- Find oxygen level, flammable and toxic gases.

8.9.7.3. Rescue Operations

- Attempt non-entry rescue using tripod and winch.
- Attach rescue line/harness if already connected.
- If entry rescue is needed:
- Only trained rescue team to enter.
- BA, rescue line, and standby person mandatory

8.9.7.4. Casualty Management

- Extract casualty using rescue stretcher.
- Provide first aid and oxygen.
- Transfer to ambulance / hospital as needed.

8.9.8. RESCUE EQUIPMENT REQUIRED

- EQUIPMENT
- Tripod and winch system

- Rescue harness and lifeline
- Gas monitor (calibrated)
- Breathing apparatus (BA)
- Escape sets
- Rescue stretcher
- Oxygen cylinder
- AED
- First Aid Kit

All equipment shall be available, inspected, and ready for use before any confined space entry.

8.9.9. TRAINING & COMPETENCY REQUIREMENTS

Sl. No..	ROLE	REQUIRED TRAINING
1	CSE Rescue Team	Confined Space Rescue
2	BA Wearers	BA certification & refresher
3	Standby Person	Confined Space Awareness
4	First Aiders	First Aid / BLS
5	Supervisors	Permit-to-Work & Emergency Response
6	Traffic Diversion Teams	TM Engineer

Training records shall be maintained by the HSE Department.

8.9.10. COMMUNICATION & ESCALATION

Internal escalation as per EMP Section 4.7

- Emergency services contacted as required.
- Client / Consultant notification through Incident Commander
- Emergency contact numbers are displayed at all site locations.

8.9.11. POST-INCIDENT ACTIONS

- Secure the area.
- Suspend confined space activities.
- Conduct incident investigation!
- Review PTW, RA, and rescue effectiveness.
- Implement corrective and preventive actions.

8.9.12. DRILLS & REVIEW

- Confined Space Rescue Drill: 6-monthly
- Procedure reviewed after:
- Drill outcomes
- Actual incident
- Change in scope or method

		
CHINA CIVIL ENGINEERING CONSTRUCTION CORPORATION–Dubai Branch R1181/2 Project Emergency Preparedness and Response Plan (PEPRP)	Doc. Ref: CCECC-R1181/2-PEM-PLN-07 Rev. No.: 00 Date: 23 December 2025	

8.10 ERP- MOBILE / CRAWLER CRANE EMERGENCY & RESCUE PROCEDURE

ERP-P09 – MOBILE / CRAWLER CRANE EMERGENCY & RESCUE PROCEDURE

Project: R1181/2 – Improvement of Al Safa Road

Document Ref: CCECC-R1181/2-ERP-P09

Linked Document: Project Emergency Preparedness and Response Plan (PEPRP)

8.10.1. PURPOSE

This procedure defines the immediate response, rescue arrangements, roles, equipment, and training requirements for emergencies involving mobile or crawler cranes, including crane overturning, load drop, mechanical failure, boom collapse, or operator injury.

The objective is to protect life, secure the incident area, and conduct safe rescue without causing secondary incidents.

8.10.2. SCOPE

This ERP applies to:

- All mobile and crawler crane operations
- Lifting activities using cranes and lifting accessories
- Employees, subcontractors, and authorised visitors
- Day and night operations
- This procedure shall be read in conjunction with:
- Lifting Permit / Lift Plan
- Crane Load Charts and Manufacturer Instructions
- Approved Method Statements
- Emergency Preparedness and Response Plan (EPRP)

8.10.3. TRIGGER / ACTIVATION CRITERIA

Activate this procedure immediately if any of the following occur:

- Crane overturning or instability
- Boom, jib, or load collapse.
- Mechanical or hydraulic failure affecting safety.
- Operator injury or medical emergency inside crane cabin
- Uncontrolled load movement
- Incident Level: Level 3 to Level 4
(Level 4 where there is fatality, multiple casualties, or public impact)

8.10.4. KEY HAZARDS

- Secondary collapse or further crane movement
- Suspended or unstable loads
- Electrical hazards (overhead lines)
- Crushing and impact injuries
- Restricted access for rescue

8.10.5. ROLES & RESPONSIBILITIES

Sl. No..	ROLE	IMMEDIATE RESPONSIBILITIES
1	Incident Commander	Overall command and authority liaison

Sl. No..	ROLE	IMMEDIATE RESPONSIBILITIES
2	Emergency Coordinator	Activate ERT and emergency services
3	Lifting Supervisor	Secure lifting area, stop all lifts
4	Crane Operator (if able)	Shut down crane safely
5	Rescue Team	Conduct rescue operations
6	First Aider / Nurse	Casualty care and stabilisation
7	HSE Officer	Documentation and investigation support

8.10.6. RESCUE STRATEGY (ALARP PRINCIPLE)

- Stop all lifting operations at once.
- Secure the load and crane movement where possible.
- Establish a large exclusion zone.
- Rescue actions must not expose responders to unstable crane or load.
- Emergency services to be involved without delay for serious incidents.

8.10.7. STEP-BY-STEP RESPONSE ACTIONS

8.10.7.1. Immediate Actions

- Stop work and raise alarm.
- Evacuate all personnel from the crane danger zone.
- Isolate crane power and hydraulics (if safe)
- Prevent unauthorised access.

8.10.7.2. Scene Control

- Establish exclusion zone around crane and load.
- Suspend all nearby activities.
- Assess stability of crane and load from a safe distance.

8.10.7.3. Rescue Operations

- If operator is injured inside cabin:
- Attempt communication
- Rescue only by trained height rescue personnel.
- Do not attempt to move the crane to rescue.
- Await emergency services if access is unsafe.

8.10.7.4. Casualty Management

- Stabilise casualty once safely accessed.
- Apply first aid and immobilisation as required.
- Transfer casualty using rescue stretcher.
- Arrange ambulance / hospital transfer as required.

8.10.8. RESCUE EQUIPMENT REQUIRED

- Rescue stretcher
- Height rescue kit (ropes, descenders)
- Spinal collar

- Oxygen cylinder
- AED
- First Aid Kit
- All equipment must be available, inspected, and ready before lifting activities.

8.10.9. TRAINING & COMPETENCY REQUIREMENTS

Sl. No..	ROLE	IMMEDIATE RESPONSIBILITIES
1	Crane Operators	Valid operator certification
2	Lifting Supervisors	Lifting Supervision Training
3	Rescue Team	Height Rescue
4	First Aiders	First Aid / BLS
5	Riggers / Signalmen	Lifting & Signalling

8.10.10. COMMUNICATION & ESCALATION

- Follow escalation protocol as per EMP Section 4.7
- Emergency services contacted as required.
- Client / Consultant notified through Incident Commander
- Crane supplier/manufacturer notified by Project Management

8.10.11. POST-INCIDENT ACTIONS

- Suspend crane operations.
- Secure and barricade crane and lifting area.
- Conduct incident investigation.
- Review Lift Plan, crane certification, and ground conditions.
- Implement corrective and preventive actions.

8.10.12. DRILLS & REVIEW

- Crane Emergency Drill: Annual (or after major lift change)
- Procedure reviewed after:
- Drill outcomes
- Actual incidents
- Change in crane type or lifting method.

		
CHINA CIVIL ENGINEERING CONSTRUCTION CORPORATION–Dubai Branch R1181/2 Project Emergency Preparedness and Response Plan (PEPRP)	Doc. Ref: CCECC-R1181/2-PEM-PLN-07 Rev. No.: 00 Date: 23 December 2025	

8.11 ERP- P11 - PANDEMIC / INFECTIOUS DISEASE RESPONSE PROCEDURE

Project: R1181/2 – Improvement of Al Safa Road

Document Ref: CCECC-R1181/2-EPRP-ERP-11

Parent Document: Emergency Preparedness and Response Plan (EPRP)

Incident Level: Level 1 to Level 3

8.11.1. PURPOSE

This procedure establishes a **structured and controlled response** to pandemic or infectious disease outbreaks (e.g. COVID-19, influenza, MERS-CoV or similar) to:

- Protect the health and safety of the workforce and public.
- Prevent transmission within project sites, camps, and transport.
- Ensure continuity of critical project operations.
- Comply with DHA, MOH, NCEMA, RTA, and UAE Federal requirements.

8.11.2. SCOPE

This procedure applies to:

- All project worksites, offices, welfare facilities, labour camps, and transport
- Employees, subcontractors, visitors, consultants, and third parties
- Day and night shifts, including off-site accommodations.

8.11.3. DEFINITIONS

Sl. No..	TERM	DEFINITION
1	Suspected Case	Person showing symptoms consistent with infectious disease
2	Confirmed Case	Laboratory-confirmed infection
3	Close Contact	Person within 2 m for ≥15 minutes
4	Isolation	Separation of suspected/confirmed case
5	Quarantine	Restriction of movement for exposed persons

8.11.4. TRIGGERS FOR ACTIVATION

Activate this procedure when any of the following occur:

- Worker reports fever, cough, breathing difficulty, fatigue.
- Positive test result reported.
- Notification from health authority
- Multiple similar symptoms detected on site.
- Government health advisory issued.

8.11.5. ROLES & RESPONSIBILITIES

Sl. No..	ROLES	RESPONSIBILITY
1	Project Director	Strategic decisions, authority liaison
2	Project HSE Manager	Overall control, reporting, compliance
3	Site Nurse / Medical Staff	Medical assessment, monitoring

Sl. No..	ROLES	RESPONSIBILITY
4	Emergency Coordinator	Isolation activation, communication
5	Supervisors	Immediate reporting, workforce control
	HR / Camp Manager	Accommodation isolation & records

8.11.6. IMMEDIATE RESPONSE ACTIONS

❖ Identification & Reporting

- Any symptomatic person must immediately inform supervisor or HSE.
- Supervisor to stop work and prevent close contact.
- HSE Manager and Site Nurse to be notified.

❖ Isolation

- Suspected person to be moved to designated isolation room.
- Provide face mask, gloves, and hand sanitiser.
- Maintain minimum 2 m distance.

8.11.7. MEDICAL ASSESSMENT & ESCALATION

Sl. No..	TERM	DEFINITION
1	Mild symptoms	Monitor, isolate, medical advice
2	Severe symptoms	Call 998 (Ambulance)
3	Confirmed case	Follow DHA / MOH protocol
4	Multiple cases	Escalate to Incident Commander

8.11.8. CONTACT TRACING & QUARANTINE

- Find all close contacts within earlier 48–72 hours.
- Suspend affected work group if needed.
- Quarantine contacts as per DHA guidance.
- Maintain confidential contact-tracing records.

8.11.9. WORKSITE & CAMP CONTROL MEASURES

Sl. No..	CONTROL AREA	MEASURES
1	Site	Reduced manpower, distancing
2	Transport	Reduced seating, disinfection
3	Welfare	Scheduled use, enhanced cleaning
4	Camp	Isolation rooms, access control

8.11.10. HYGIENE & PREVENTION CONTROLS

- Hand washing facilities and sanitisers.
- Routine disinfection of high-touch surfaces
- Mask usage as per authority guidance.
- Awareness posters and toolbox talks

8.11.11. BUSINESS CONTINUITY MEASURES

- Find critical operations.
- Crosstrain essential staff
- Stagger shifts and work zones.
- Maintain minimum workforce for safety-critical tasks.

8.11.12. COMMUNICATION & REPORTING

Sl. No.,	COMMUNICATION	RESPONSIBLE
1	Internal notification	Emergency Coordinator
2	Authority reporting	Project Director / HSE
3	Client / Consultant	Project Director
4	Workforce updates	HSE Department

8.11.13. TRAINING & AWARENESS

Sl. No.,	TARGET GROUP	TRAINING
1	All workers	Infection awareness
2	Supervisors	Symptom recognition
3	Medical staff	Infection control
4	Camp staff	Hygiene management

8.11.14. RECORDS & DOCUMENTATION

- Medical logs
- Isolation records
- Contact-tracing sheets.
- Cleaning & disinfection logs
- Authority communications

8.11.15. STAND-DOWN & RETURN-TO-WORK

- Clearance only with medical approval
- Fit-to-work confirmation needed.
- Gradual reintegration if necessary

8.11.16. POST-INCIDENT REVIEW

- Review effectiveness of controls.
- Update risk assessment if required.
- Conduct management review.
- Implement corrective and preventive actions.

8.11.17. DRILLS & REVIEW

- Pandemic response drill – Annual / as needed.
- Review procedure following:
 - Authority updates
 - Actual incidents
 - Lessons learned

								
CHINA CIVIL ENGINEERING CONSTRUCTION CORPORATION–Dubai Branch R1181/2 Project Emergency Preparedness and Response Plan (PEPRP)		<table><tr><td>Doc. Ref:</td><td>CCECC-R1181/2-PEM-PLN-07</td></tr><tr><td>Rev. No.:</td><td>00</td></tr><tr><td>Date:</td><td>23 December 2025</td></tr></table>	Doc. Ref:	CCECC-R1181/2-PEM-PLN-07	Rev. No.:	00	Date:	23 December 2025
Doc. Ref:	CCECC-R1181/2-PEM-PLN-07							
Rev. No.:	00							
Date:	23 December 2025							

SECTION 09 – ANNEXURES

- 10.1 ANNEXURE A – EMERGENCY CONTACT LIST
- 10.2 ANNEXURE B – OFFICE EMERGENCY EVACUATION LAYOUT PLAN
- 10.3 ANNEXURE C – NEAREST HOSPITAL LOCATION LAYOUT PLAN
- 10.4 ANNEXURE D – EMERGENCY DRILL REPORT FORM
- 10.5 ANNEXURE E – INCIDENT / ACCIDENT REPORT FORM
- 10.6 ANNEXURE F – EMERGENCY MUSTER POINT ROLL CALL SHEET
- 10.7 ANNEXURE G – EMERGENCY RESPONSE - IN CASE OF FIRE
- 10.8 ANNEXURE H – EMERGENCY ACTION PLAN
- 10.9 ANNEXURE I – EMERGENCY DRILL PLAN
- 10.10 ANNEXURE J – PROJECT EMERGENCY RESPONSE COMMUNICATION CHART
- 10.12 ANNEXURE L – FIRST AID KIT INSPECTION CHECKLIST
- 10.11 ANNEXURE K – EMERGENCY RESPONSE TEAM
- 10.11 ANNEXURE K – EMERGENCY TOOLS AND EQUIPMENTS
- 10.11 ANNEXURE K – FIRE RISK/ IMPACT ASSESSMENT

 		
Emergency Contact Numbers		

Contract No.:	R 1181-2	Project Title:	IMPROVEMENT OF AL SAFA STREET
---------------	----------	----------------	-------------------------------

SR. PROJECT MANAGER

Mohsen D Gazzaz	Mobile	052 282 5807
-----------------	--------	--------------

DEPUTY PROJECT MANAGER

Ahmad Elkadi	Mobile	050 907 0342
Guo Pingcheng	Mobile	058 103 0678

HSE PERSONAL

Mirza Shahabuddin Balg (Office & Site)	Mobile	055 933 1082
Ajmal Rashid (Office & Site)	Mobile	056 148 7012
Shahid Ahmad (Site Day)	Mobile	050 560 9961
Basharat Karim (Site Day)	Mobile	054 358 9874
Asif (Site Night)	Mobile	052 787 0311

CONSTRUCTION MANAGER

Ahmad Ghanem (Utility & Road Workers)	Mobile	055 665 1144
Enji Shi (Structure)	Mobile	054 738 1666

MALE NURSE

VIJAY SINGH	Mobile	058 837 2856
-------------	--------	--------------

SITE ENGINEER

Kasim (Utility & Road Workers)	Mobile	056 143 5466
Syed Abdul Kather (Electrical)	Mobile	055 789 3827
Hashim Ali (Structure)	Mobile	055 288 9793
T Sadik (Structure)	Mobile	050 812 2973
Ibrahim Khashan (Utility & Road Workers)	Mobile	055 466 0767

SUPERVISOR

Zakir Ali (Structure)	Mobile	055 168 6375
-----------------------	--------	--------------

SAFETY HOT LINE (24 Hours)	Mobile	(Project specific)
-----------------------------------	--------	---------------------------

EMERGENCY SERVICES

POLICE		999
CIVIL DEFENCE		997
AMBULANCE		998
DUBAI MUNICIPALITY		900
POISON CONTROL		800 424
RTA		800 9090
Iranian Hospital - Dubai	NEAREST HOSPITAL	04 344 0250

SITE WATCH MAN

Deepak Yadav (Day)	Mobile	058 282 8081
Harshdeep (night)	Mobile	055 610 1653


SITE ELECTRICIAN

Sanjay (Day)	Mobile	052 368 7302
Sonu	Mobile	050 835 6438
Metash (Night)	Mobile	050 393 2585

OFFICE EMERGENCY EVACUATION PLAN

PROJECT NUMBER & TITLE:

R-1181/2 IMPROVEMENT OF AL SAFA ROAD

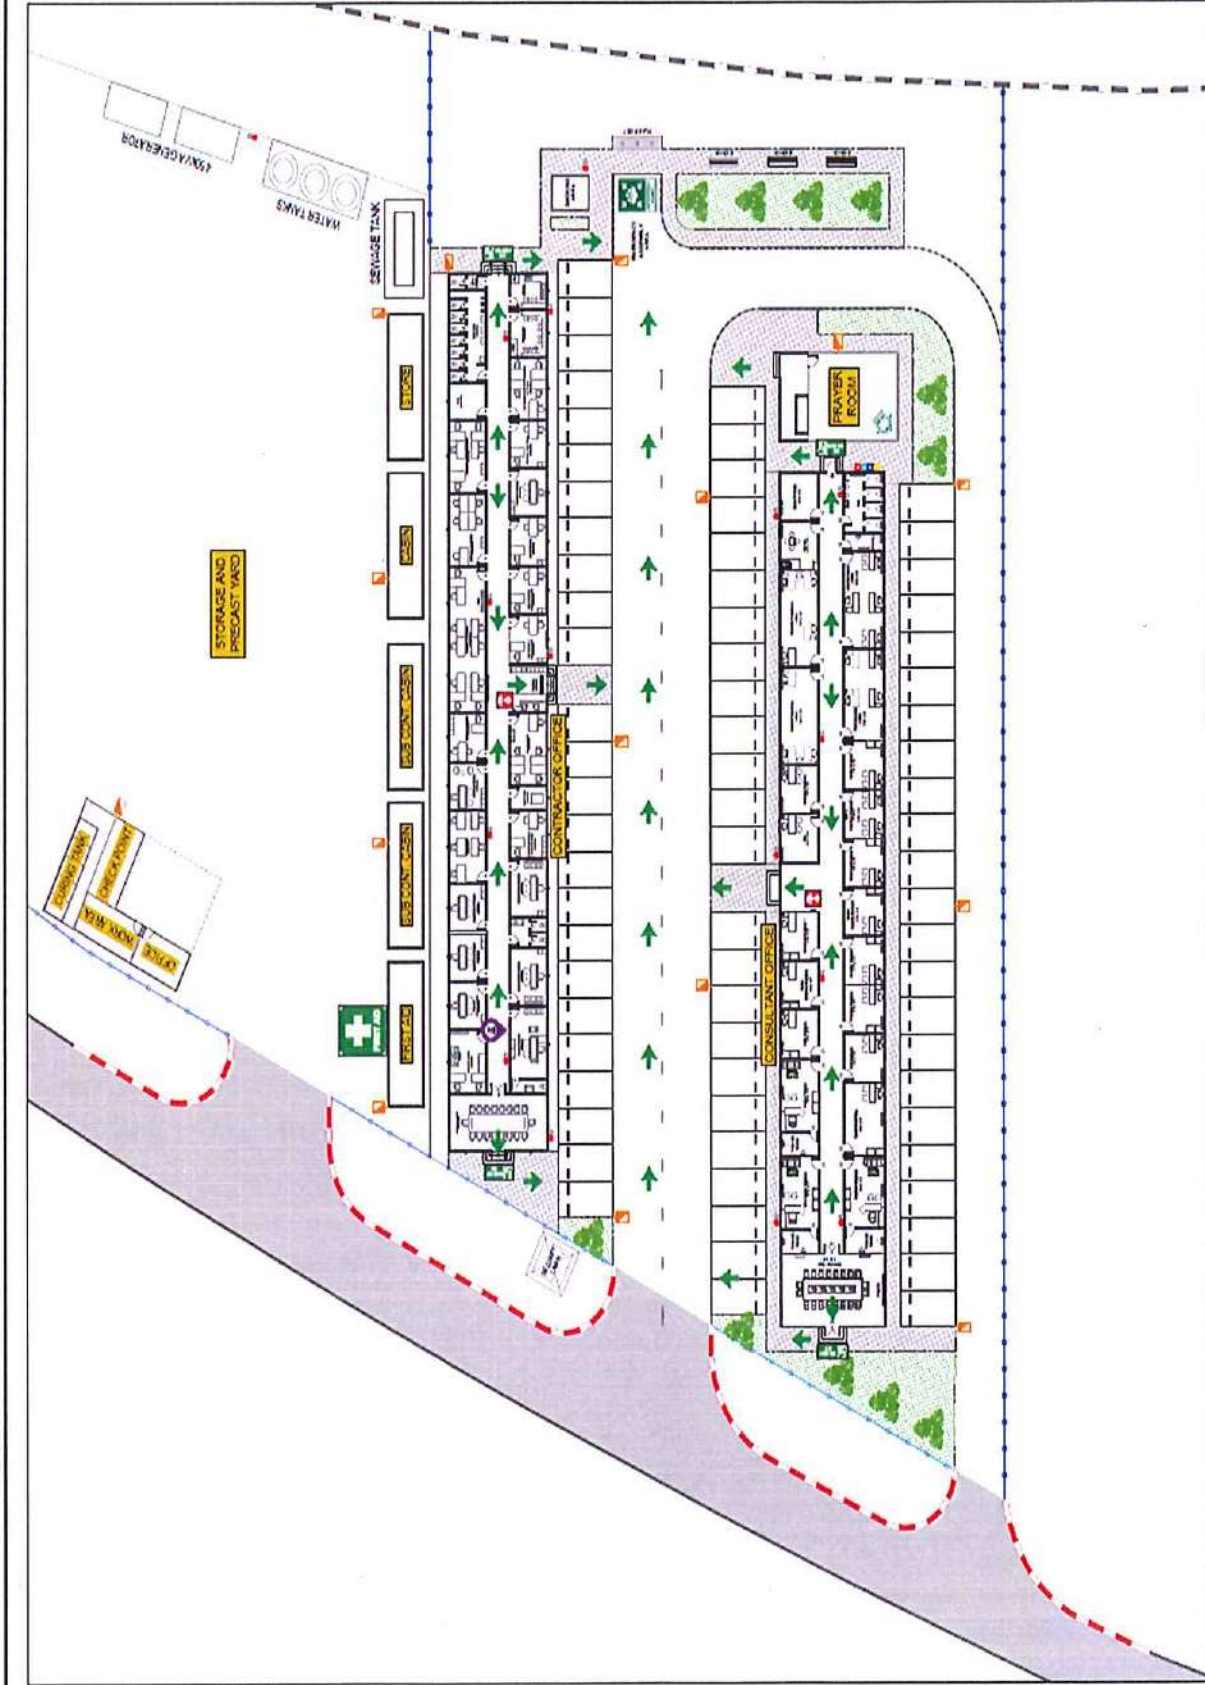

NOTES:
1. ALL DIMENSIONS & LEVELS ARE IN METERS UNLESS NOTED OTHERWISE
2. ALL COORDINATES ARE BASED ON DUBAI LOCAL TRANSVERSE MERCATOR
3. ALL LEVELS ARE BASED ON DUBAI MUNICIPALITY DATUM (DMC)

- LEGEND:
- FIRST AID ROOM
 - ASSEMBLY POINT
 - FIRE EXTINGUISHER
 - FIRE ALARM
 - EMERGENCY EXIT

SHOP DRAWING

NO.	DATE	DESCRIPTION	BY	CHKD
1	01-12-2025	ISSUED FOR TENDER	MM	MM

CLIENT: RTA
CONSULTANT: PARSONS
CONTRACTOR: CCECC

PROJECT: IMPROVEMENT OF AL WASHL JUMRAH, AL SAFA & UMM SUKHEIM ROADS (IMPROVEMENT OF AL SAFA ROAD)

CONTRACTOR: CCECC

PROJECT TITLE: R1181-2


CONTRACTOR OFFICE
EMERGENCY EVACUATION PLAN

DRAWN: DO	CHECKED: AJ	APPROVED: MG
DATE: 01-12-2025	DO REF NO: -	
SCALE: NTS		

DRAWING NO: CCECC-R1181-2-CC-GEN-LP-004
REV NO: 00

NEAREST HOSPITAL LOCATION LAYOUT PLAN

PROJECT NUMBER & TITLE: R-1181/2 IMPROVEMENT OF AL SAFA ROAD

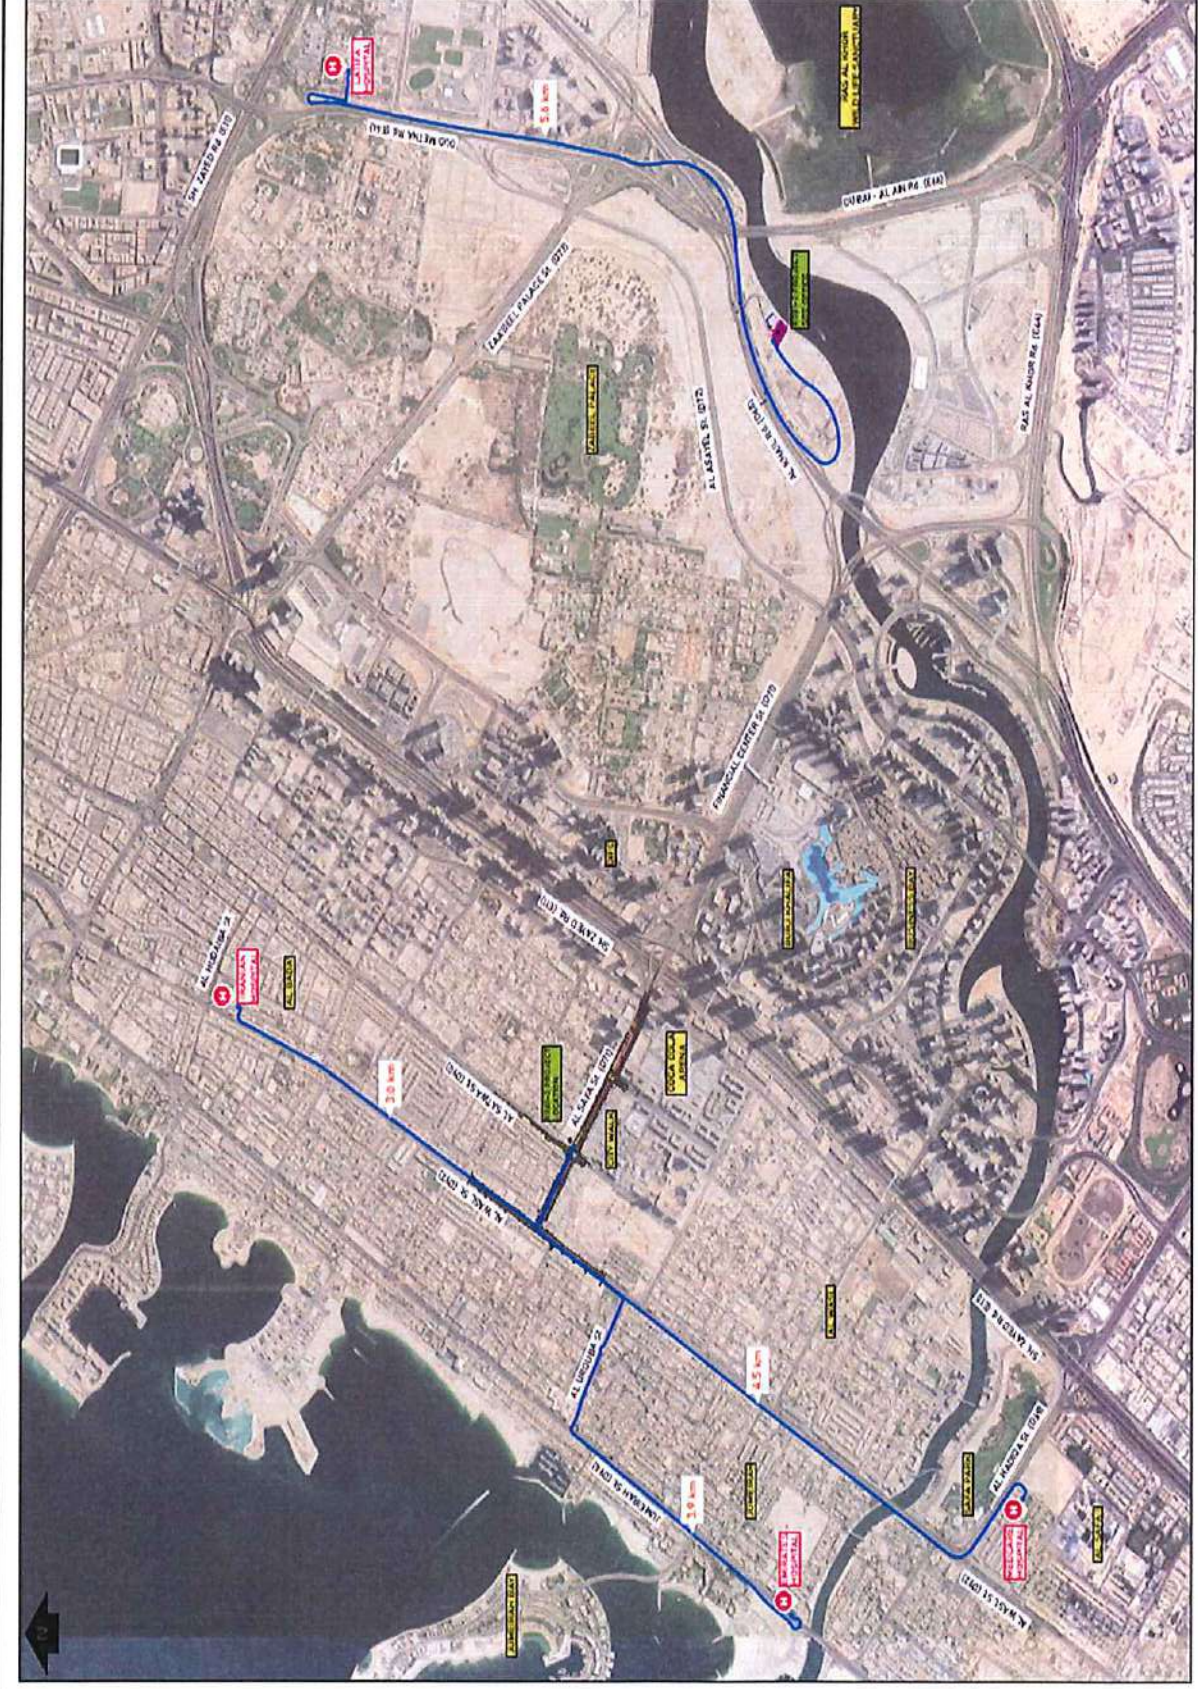

NOTES:
1. ALL DIMENSIONS & LEVELS ARE IN METERS UNLESS NOTED OTHERWISE
2. ALL COORDINATES ARE BASED ON DUBAI LOCAL TRANSVERSE MERCATOR
3. ALL LEVELS ARE BASED ON DUBAI MUNICIPALITY DATUM (DMDS)

[SHOP DRAWING]

NO.	01	DATE	01-12-2020	FOR APPROVAL	RTA
BY	01	DATE	01-12-2020	FOR APPROVAL	RTA
CLIENT	RTA				

CONSULTANT
PARSONS

CONTRACTOR
CCECC

PROJECT LOCATION
IMPROVEMENT OF AL WASH, SUMERAM,
AL SAFA & UMM SUQUH ROADS
(IMPROVEMENT OF AL SAFA ROAD)

PROJECT NO.
R1181-2

DRAWING TITLE
NEAREST HOSPITAL LOCATIONS
LAYOUT PLAN

DRAWN BY	DESIGNED BY	APPROVED BY
DATE: 01-12-2020	DATE: 01-12-2020	DATE: 01-12-2020
SCALE: NTS	SCALE: NTS	SCALE: NTS

REV NO.
00

CCECC-R1181-2-CC-GEN-LP-005



Emergency Drill Reporting Form

Attach to this form a list of all staff who participated in the drill, and any visitors participating.

Project Name& No.:	Drill Location:	Mock Drill Ref No:
Name of Emergency Coordinator:	Drill Concluded:	Drill Date:
Name of Fire Warden:	Time Alarm Sounded:	Time to Evacuate:

Type of Drill:	Notification / Alert Method:	Weather Conditions:
☐ Fire / Evacuation ☐ Suspension trauma ☐ Confined Space rescue ☐ Electric Shock ☐ Excavation collapse rescue ☐ Environmental spill ☐ Land ☐ Marine ☐ Medical Emergency ☐ Rescue from Water ☐ Vessel Emergencies ☐ Diving Emergencies ☐ Weather Emergency ☐ Other: _____	☐ Bell or Buzzer ☐ Enhanced Alert System ☐ Intercom ☐ Phone ☐ Voice Notification ☐ Siren ☐ Other: _____	☐ Clear ☐ Cloudy ☐ Raining ☐ Rain and wind ☐ Windy ☐ Others: _____
	Participants: (check all that apply)	Situation at Start of Drill:
	☐ Senior / Line Management ☐ ERP team ☐ Safety Personnel ☐ Employees / Staff ☐ Client / 3 RD Party ☐ Subcontractor ☐ Other: _____	☐ Before Business Hours ☐ During Business Hours ☐ Peak Business Hours ☐ Lunch Time ☐ After Business Hours ☐ Other: _____ Describe the site area condition/ situation on the start of the drill

Brief Description / Scenario on Emergency Situation (If required)

Mock Drill Pictures

--	--	--

Performance of Responses & Strategy Procedures Followed: ☐ Satisfactory ☐ Unsatisfactory ☐ Needs Improvement	Mock Drill: ☐ Organized ☐ Unorganized
---	---

Positive Observation (If any)



Emergency Drill Reporting Form

Problems Encountered: (Check all that apply)

- | | |
|--|---|
| ☐ Congestion in hallways
☐ Alarm not heard
☐ Employees unsure of what to do / proper
☐ Emergency equipment not available
☐ Doors / Windows left open
☐ No awareness towards ERP contact list
☐ Incident communication protocol not adhered
☐ Personnel not accounted for / attendance
☐ Difficulties with evacuation of disabled personnel, customers, or visitors
☐ Area not cordoned / secured
☐ ERT Fails to perform duties and responsibilities
☐ No / Lack of Directional Signages | ☐ Radio communication problems
☐ Un organized Personnel movement
☐ Long time to evacuate building
☐ Exceeds the optimum evacuation time/ rescue
☐ Personnel not serious about drill
☐ Insufficient or unavailable supplies
☐ Emergency Doors or Exits blocked
☐ Delay of Emergency Response Vehicle
☐ Interagency miscommunications
☐ Assembly point too close
☐ Other: _____
_____ |
|--|---|

Corrective Action for Problems Encountered

Responsible Person

Target Date

Mitigation / Plans for Improvement: (check all that apply and explain below)

- | | |
|---|---|
| ☐ Duty of Care
☐ Additional training required
☐ Increase awareness familiarity to drill / more drills
☐ Additional rescue equipment & Emergency supplies | ☐ Improved Cooperation required from personnel
☐ Review / Revise Emergency Procedures
☐ Other: _____ |
|---|---|

Explanation of Mitigation / Plans for Improvement

Responsible Person

Target Date

Lessons Learnt / Area for Improvement/Other Comments

Reviewed By:

Date :

Signature :

Approved By:

Date :

Signature :

Remarks / Comments

Remarks / Comments

 حكومة دبي GOVERNMENT OF DUBAI	 هيئة الطرق والمواصلات RTA	 PARSONS	 中国土木 CCECC
INCIDENT REPORT			

SECTION A - INCIDENT DETAILS: (Shall be reported to Group HSEQ Manager via What's App or email within 4hrs)					
1	Project Name & No.:	Date of incident:	Incident Report No.:	Company Name: ☐ CCECC ☐ Subcontractor	Reportable to Reg. Authority ☐ Yes ☐ No
2	☐ Injury / Illness ☐ Property Damage ☐ Environmental ☐ Other Incidents: (☐ Near miss ☐ HiPo ☐ Theft)				
3	☐ Fatality ☐ LTI (3d) ☐ LTI(1d) ☐ MTC ☐ FA ☐ Ill Health ☐ VAW ☐ RWC (LTI – Lost Time Injury; MTC – Medical Treatment Case; FA – First Aid; VAW – Violence at Work; RWC – Restricted Work Case; HiPo – High Potential)				
4	Classification by Severity: Actual: Potential: 1 2 3 4 5 1 2 3 4 5 Actual: Potential:	Supervisor's Name:	Witness Name(s):	Time of Incident:	
5	Initial Notification Description of Incident			Location of Incident	

SECTION B - INVESTIGATION				
Involved/ Injured Party Name:	Trade Involved:	Test Cert. Exp. Date:	Plant Model/Make:	Registration:
Full Investigation Description of Incident				
Incident Cause Analysis (Brief Explanation of the Cause of Incident - Please Tick Relevant Boxes below)				
Immediate Cause Explanation:				
Root Causes / Contributing Factors Categories				
☐ Inadequate Planning Controls ☐ Inadequate Design / Engineering Controls ☐ Inadequate Resource Management (Men Materials Equipment) ☐ Time / program pressure	☐ Inadequate Management / Supervision Controls ☐ Inadequate Knowledge / Training ☐ Work Environment ☐ Others.....	☐ Risk perception Lack of Belief Complacency ☐ Inadequate Tools Plant Equipment Controls ☐ Process / System failure ☐ Personal Factor (Stress Fatigue)		
Root Causes / Contributing Explanation				

INCIDENT REPORT

NATURE OF INJURY / ILLNESS ☐ Abrasions ☐ Bruising ☐ Amputation ☐ Bite / Sting ☐ Burn ☐ Concussion ☐ Crush ☐ Cut ☐ Heat related illness ☐ Laceration ☐ Hearing Loss / Deafness ☐ Dislocation ☐ Electric Shock ☐ Fracture ☐ Foreign Body in eye ☐ Foreign Body under skin ☐ Hernia ☐ Infectious Disease ☐ Musculoskeletal Disorder ☐ Nerve / Spinal Cord Injury ☐ Industrial Illness ☐ Poisoning / Toxic Effect ☐ Psychological (Stress) ☐ Respiratory Disease ☐ Unconsciousness ☐ Skin Irritation ☐ Strain ☐ Sprain ☐ Others _____		PARTS OF BODY INJURED ☐ Head ☐ Face ☐ Eyes ☐ Ears ☐ Neck ☐ Shoulder ☐ Chest ☐ Abdomen ☐ Groin ☐ Back (Upper) ☐ Back (Lower) ☐ Buttock ☐ Skeletal System ☐ Finger ☐ Hand ☐ Wrist ☐ Arm ☐ Toe ☐ Feet ☐ Lower Leg ☐ Upper Leg ☐ Lungs ☐ Nervous System ☐ Skin ☐ Others _____
PROPERTY DAMAGE ☐ Building Materials ☐ Construction Materials ☐ Plant Equipment ☐ Underground Utilities ☐ Traffic Material ☐ Others _____	ENVIRONMENTAL ☐ Spills ☐ Noise ☐ Heritage ☐ Release / Discharge ☐ Emission ☐ Contamination of land / water ☐ Damage to agriculture	NEAR MISS ☐ Unsafe Act / Practice ☐ Unsafe Condition
ACTIVITY ☐ Lifting ☐ Excavation ☐ Drilling ☐ Driving – Light Vehicles ☐ Driving / Operation – Heavy Equipment ☐ Pilling ☐ Diving ☐ Hot Works ☐ Confined Space ☐ Marine Vessel - Operation ☐ Electrical Works ☐ Mechanical Works ☐ Maintenance Work ☐ Wood Works ☐ Concreting ☐ Form Work ☐ Work at height ☐ Temporary Works ☐ Dredging ☐ Manual Handling ☐ Roads Works ☐ Material Handling / Storage ☐ Marine Vessel - Navigation ☐ Power Tool Operation ☐ Forklift Operation ☐ Others _____		
SECTION C – CORRECTIVE ACTION AND CLOSE OUT		
Immediate Correction Action	Owner	Time Scale
Corrective Action	Owner	Time Scale



هيئة الطرق والمواصلات
ROADS & TRANSPORT AUTHORITY



PARSONS®



中国土木
CCECC

INCIDENT REPORT

Incident Cost (Attach Cost Calculator; Reference Form No.)	Number of Man Days Lost:
Has Method Statement task sheet reviewed / updated? ☐ Yes ☐ No	Is Risk assessment reviewed / Updated? ☐ Yes ☐ No
Are incident report communicated to all parties ☐ Yes ☐ No	Is Learning Event prepared? ☐ Yes ☐ No
HSE Officer Comment: Name & Signature:	Verification of corrective action done: ☐ Yes ☐ No Incident close out: ☐ Yes ☐ No Incident Register updated: ☐ Yes ☐ No Is there any insurance claims: ☐ Yes ☐ No
Project Manager's Comment: Name & Signature:	

PHOTOS EVIDENCE

CORRECTIVE ACTION EVIDENCE

 		 
EMEGENCY MUSTER POINT ROLL CALL SHEET		Doc. No: CCECC/EHS
PROJECT NAME: R1181-2 IMPROVEMENT OF AL SAFA STREET		Revision: 0
LOCATION: AL SAFA STREET		Effective Date: 16.09.2025

S-NO	Name	PRESENT	ABSENT	EFFECTED	SIGNATURE
1					
2					
3					
4					
5					
6					
7					
8					
9					
10					
11					
12					
13					
14					
15					
16					
17					
18					
19					
20					

COMMENTS:

 حكومة دبي GOVERNMENT OF DUBAI	 هيئة الطرق والمواصلات ROADS & TRANSPORT AUTHORITY		 中国土木 CCECC
EMERGENCY REPORTING (Incuse of Fire)			

Contract No.:		Project Title:	
---------------	--	----------------	--

INCASE OF FIRE

-  Shout, "Fire...Fire...Fire"
-  Activate fire alarm pull station if in a building
-  Shut off equipment, close your door and Alert others
-  Assist others in evacuating if possible and immediately leave the building
-  Try to put the fire out with available fire fighting equipment (fire extinguisher) if it is safe to do so.
-  If the fire is too large to handle, call Emergency Services (see below)
-  Assemble at designated ASSEMBLY Point; account for others from your office, floor, etc.
-  Person with knowledge of the situation should meet with Fire Warden/ Marshal.
-  DO NOT re-enter the building until cleared by Fire Warden/ Marshal.

IN CASE OF AN ACCIDENT

-  Do not panic.
-  Inform others who may be in danger.
-  Inform your Supervisor/First Aider who will activate the emergency plan immediately.
-  Provide relevant first aid if competent to do so.
-  If possible do not move the injured person.
-  If required, call emergency services.
-  Stay with injured person until medical assistance arrives.
-  Try to keep injured person calm.

SITE OFFICE		
SAFETY HOT LINE (24 Hours)		
Email:		
EMERGENCY SERVICES		
POLICE		999
CIVIL DEFENCE		997
AMBULANCE		998
DUBAI MUNICIPALITY		900
ABU DHABI MUNICIPALITY		993

Contract No.:		Project Title:	
---------------	--	----------------	--

IN CASE OF ANY ACCIDENT/INCIDENT

- ☞ Inform your supervisor who will summon the first aider immediately.
- ☞ Inform your manager.
- ☞ Inform the following emergency services if required.

SITE OFFICE	
SAFETY HOT LINE (24Hours)	
Email:	

EMERGENCY SERVICES		
POLICE		999
CIVIL DEFENCE		997
AMBULANCE		998
DUBAI MUNICIPALITY		900

MESSAGE TO BE GIVEN

- ☞ Your name
- ☞ Company name
- ☞ Your phone number
- ☞ Exact location/site
- ☞ Nature of accident/incident.
- ☞ Wait for few minutes to receive return instructions from the emergency services.
- ☞ Deploy a person to receive emergency services at a nearby prominent location.

DRILL PLAN FOR YEAR-2026

PROJECT NUMBER & TITLE:

R-1181/2 IMPROVEMENT OF AL SAFA ROAD

List of Drills	Months											
	JAN-26	FEB-26	MAR-26	APR-26	MAY-26	JUN-26	JUL-26	AUG-26	SEP-26	OCT-26	NOV-26	DEC-26
Traffic Incident		12th Feb 2026						17th Aug 2026				
Electrocution / Electric Shock						14th Jun 2025					2nd Nov 2026	
Excavation collapse	2nd Jan 2026				08th May 2026							
Environmental-Spillage									13th Sep 2026			
Fire / Evacuation					26th May 2026					17th Oct 2026		
Confined Space												6th Dec 2026
Fall from Height			7th Mar 2026								22nd Nov 26	
Medical/ Heat Stress							9th Jul 2026					
Utility Strike				10th Apr 2026								
Extreme Weather Condition		12th Feb 2026										
Pandemic												

As per any Pandemic

LEGEND:	Drill Planned →	Drill Pending →	Drill Completed →

Prepared by – Mirza Shahabuddin Baig (HSE Manager)

Approved By – Mohsen D Gazzaz (Project Director)

Sign: _____


Sign: _____

Site Specific – R 1181-2
Created by – Mirza Shahabuddin Baig

1 | Page

Revision: 0

EMERGENCY RESPONSE COMMUNICATION CHART

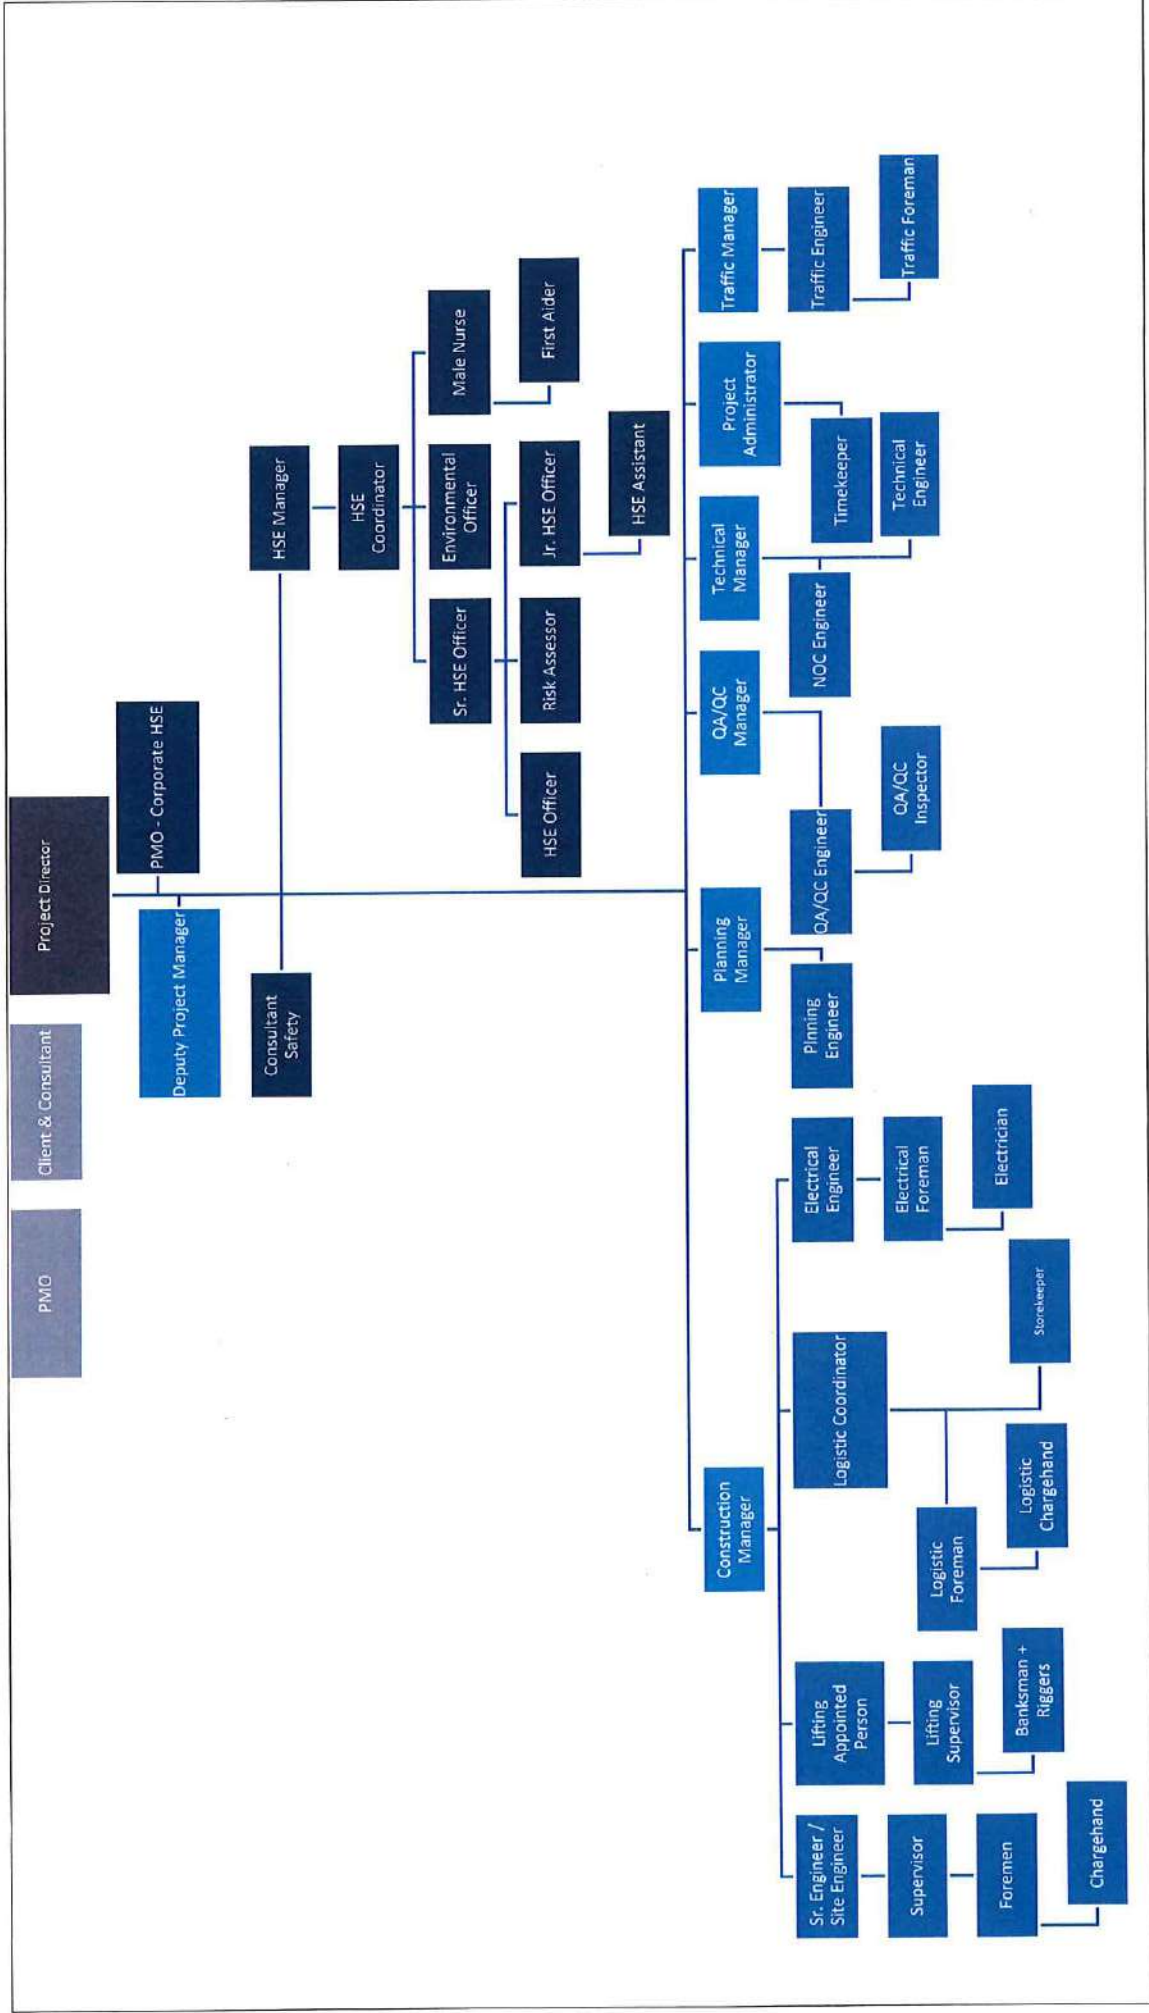

FIRST AID KIT INSPECTION

PROJECT NAME

R1181-2 IMPROVEMENT OF AL SAFA STREET

LOCTION S.N.	DESCRIPTION	QUANTITY	DATE OF EXPIRY	MONTH OF INSPECTION:			
				WEEK 1	WEEK 2	WEEK 3	WEEK 4
1	FIRST AID GUIDE	1					
2	BIO HAZARD BAG SMALL - YELLOW	4					
3	ALCOHOL SWABS	100	Jun-28				
4	BANDAGE ADHESIVE	100	May-29				
5	SPOT BANDAGE	25	May-29				
6	WOUND DRESSING STERILE 6X7 cm	3	Feb-29				
7	AMEDONE SOLUTION 100 ml	1	May-27				
8	BURN DRESSING 5X5 cm 20 gm GEL	1	Jun-27				
9	EYE PAD	6	Aug-28				
10	DISPOSABLE GLOVES (PAIR)	4					
11	BURN GEL 3.5 gm	3	Oct-28				
12	GAUZE SWAB STERILE 4X4 2" s	10	Feb-29				
13	GAUZE SWAB STERILE 2X2 2" s	20	Oct-29				
14	COTTON BANDAGE 2"	6	Jun-28				
15	COTTON BANDAGE 4"	3	Jul-29				
16	CONFORMING BANDAGE 2"	6					
17	CONFORMING BANDAGE 4"	3					
18	TRIANGULAR BANDAGE	4	Jul-29				
19	CPR MASK SMALL	1					
20	PAPER PLASTER 1/2"	1					
21	SCISSOR (SMALL)	1					
22	PLASTIC FORCEP 12 cm	1					
23	COLD PACK 5X6	2	Aug-29				
24	COTTON ROLL 100gm	1	Jul-29				
25	COTTON TIPPED APPLICATOR	1					
26	EMERGENCY BLANKET	1	Jun-29				
27	FINGER DRESSING	2	Jul-29				
28	CREPE BANDAGE COTTON 3"	2	Mar-29				

INSPECTED BY

VERIFIED BY

NAME OF STAFF :-

VIJAY SINGH

NAME OF STAFF :-

DESIGNATION :-

MALE REGISTERED NURSE

DESIGNATION :-

SIGNATURE :-

SIGNATURE :-

 		 
CHINA CIVIL ENGINEERING CONSTRUCTION CORPORATION–Dubai Branch R1181/2 EMERGENCY RESPONSE PLAN		Doc. Ref: CCECC-R1181/2-PEM-PLN-07 Rev. No.: 00 Date: 09 December 2025

EMERGENCY RESPONSE TEAM		
Sl. No.	ROLE IN EMERGENCY	RESPONSIBLE PERSON
1	Incident Commander	Mohsen D. Gazzaz (Project Director)
2	Deputy Incident Commander	Ahmed Elkadi (Deputy PM)
3	Emergency Coordinator	CM (Enji Shei) + HSE Manager (Mirza)
4	ERT Leader	Ajmal Rashed + Asif Javeed + Hashim
5	Utility Coordinator	Kasim Ayas + Syed Abdul Kather
6	Traffic Coordinator	Aiman Jat + Hany
7	Fire Warden	Pawam Kumar
8	Site Nurse	Vijay Kumar
9	Spill Responder	Basharat and Pawan
10	CSE Rescue Lead	Balram + Sharif+ Monu
11	Rescue Team Lead	Zakir + Gautam + Shahid Ahmad
12	Height Rescue Team	Balram + Razzak

 		 
CHINA CIVIL ENGINEERING CONSTRUCTION CORPORATION–Dubai Branch R1181/2 EMERGENCY RESPONSE PLAN		
	Doc. Ref:	CCECC-R1181/2-PEM-PLN-07
	Rev. No.:	00
	Date:	09 December 2025

EMERGENCY TOOLS & EQUIPMENTS		
Sl. No.	TOOLS & EQUIPMENTS	LOCATION ON SITE
1	Medical Room	Mian Office Area
2	Assembly Points (AP-01 AP-02 AP-03 AP-04 AP-05)	(Near Site Office), (Yard and store area), (Al Wasl working area), (Al Safa working area), (Al Jumeriah working area)
3	First Aid Box	Mian Office Area + Site Working Area
4	Fire Extinguisher	Mian Office + Site working Area
5	Fire Blanket	Mian Office + Site working Area
6	Fire Alarm System (Smoke Detectors)	Mian Office + Site Office
7	Fire hoses and hydrants	Main Office
8	Emergency Alarm (Siren)	Main Office + Site Work Area
9	Heat Index Flag System	Mian Office + Site Office
10	Stretcher (Folding + Basket)	Medical Room
11	Tripod + Winch	Site Store
12	Gas Monitor	Site Store
13	Breathing Apparatus	Medical Room
14	Oxygen	Medical Room
15	Rescue kit	Site Store
16	Automated External Defibrillator (AED)	Medical Room
17	Personal Protective Equipment (PPE)	Site Store
18	Communication & Signalling Devices	Site Store
19	Spill kits (absorbent pads, booms)	Chemical Storage area
20	Flashlights and Torches	Site Store



حكومة دبي

GOVERNMENT OF DUBAI



هيئة الطرق والمواصلات

ROADS & TRANSPORT AUTHORITY



PARSONS®



中国土木

CCECC

FIRE RISK / IMPACT ASSESSMENT

Contract No.

R1181/2

Project Title

IMPROVEMENT OF AL SAFA ROAD

RA Date

17/12/2025

RA Revision No.

00

*Task / Activity

Fire Prevention

Additional Details

Hazardous Chemical required? (Tick as applicable)

Y ☐ N ☐

Confined space entry required? (Tick as applicable)

Y ☐ N ☐

Plant & Equipment involved:

- Fire Extinguishers, Generator, DB, and Gas cutter, welding machine

Power tools: Grinder, Welding Machine, Gass Cutting

Health Safety Loss & Environmental Impact

OH&S

Environmental

1-3 Assessable

Low - L

Minor / <3 Days Injury

Minor

4-9 Before task commences

Medium - M

Moderate / >3 Days Injury

Moderate

10-16 Before task commences

High - H

Major / Permanent Disability Injury

Major

20-25 Immediate

Very High - VH

Catastrophic / Fatality

Catastrophic

Severity (S)

1

2

3

4

5

Likelihood (L)

1

2

3

4

5

Unlikely

May Happen

Likely

Very Likely

Certain or Imminent

Designation:

Project HSE Engineer

Name:

Shahid Ahmad

Date:

17/12/2025

Designation:

Project HSE Manager

Name:

Mirza Shahabuddin Baig

Date:

17/12/2025

Designation:

Deputy Project Manager

Name:

Ahmed Elkadi

Date:

17/12/2025

* Task: Fire Prevention

* Date: 17/12/2025

FIRE RISK / IMPACT ASSESSMENT

S N	Activity (Break activity in work sequence as in the Method statement)	Hazard /Aspect Hazard is anything with potential to cause harm or loss.	HSE Risk Risk is the harm resulting from the hazard.	EXISTING CONTROL MEASURES	Rating (see enclosed legend page for details)			Risk Value R = S x L OHS S x L	ADDITIONAL CONTROL MEASURES	RESIDUAL RISK VALUE		
					S	OHS & E	L			S	OHS & E	L
1	Smoking	Smoking at undesignated area	Fire Loss of life and property damage	- Allow smoking only in designated areas. - NO smoking sign shall be placed in No smoking zones. - Strict disciplinary action shall be taken against the violators. - Fire extinguisher shall be provided in the smoking area	4	4	4		- Smoking area needs to be kept clear of flammable material. - Smokers should be smoking inside the smoking area only. - Cigarette butts should be disposed of in the basket/tray provided for the purpose and the fire should be put out before putting it in the tray.	3	1	3
2	Housekeeping	Slip, trips unwanted materials	Fire Loss of life and property damage	- All unwanted flammable material shall be removed from site periodically. - Material shall not be stored in access and fire exits. - Waste shall be segregated as per the waste management plan.	4	5	20		- A dedicated team under the supervision of concerned foreman shall be delegated for the regular housekeeping. - Empty cement bags, paper boxes, green net, wood dust, plywood hessian cloth and other flammable material need to remove from site / office area	3	1	3
3	Located Fire extinguishers	Non availability of firefighting equipment's	Delay in dealing with the fire. Escalation of fire	Portable fire extinguishers shall be available in	4	4	16		- Sign board shall be placed. - Fire extinguishers	3	1	3

FIRE RISK / IMPACT ASSESSMENT

* Task: Fire Prevention					* Date: 17/12/2025							
S N	Activity	Hazard /Aspect	HSE Risk	EXISTING CONTROL MEASURES	Rating (see enclosed legend page for details)			Risk Value R = S x L OHS & S x L	ADDITIONAL CONTROL MEASURES	RESIDUAL RISK VALUE		
		Hazard is anything with potential to cause harm or loss.	Risk is the harm resulting from the hazard.		OHS & E					S	L	S x L
				every in easily accessible location. Fire extinguishers should never be blocked with any material.					should be placed back in the same location if relocated for construction activities,			
4	Electrical connection	Faulty electrical connection and equipment's/ over loading of distribution boards	Fire Loss of life and property damage	- ELCB shall be installed with all the DB and periodical inspection of ELCB, tools and equipment need to be carried out by competent electrician and recorded. - Damaged equipment and cable shall be removed from site/returned to store. - Do not overload the DB.	4	5	20	- Proper cable management. - Electrician to ensure adequate connection are available. - Equipment and cable should not be lying in wet area. - Cable should not be directly inserted into the socket. - Toolbox talk to be provided to electrician. - Only industrial sockets shall be used on site. - Correct rated fuses are to be used.	3	1	3	
5	Hot work Gas cutting and welding Grinding & cutting	Hot work doing by incompetent welder, permit not obtained, combustible materials	Fire Loss of life and property damage,	HWP (Hot Work Permit) to be obtained prior to start work.	4	5	20	Only competent personnel shall be carrying out the hot work operation.	3	1	3	

FIRE RISK / IMPACT ASSESSMENT

* Task: Fire Prevention					* Date: 17/12/2025									
S N	Activity	Hazard /Aspect	HSE Risk	EXISTING CONTROL MEASURES	Rating (see enclosed legend page for details)			Risk Value R = S x L	ADDITIONAL CONTROL MEASURES			RESIDUAL RISK VALUE		
			Risk is the harm resulting from the hazard.		OHS & E		OHS & S x L					OHS & E	S	L
					S	L								

FIRE RISK / IMPACT ASSESSMENT

* Task: Fire Prevention						
S N	Activity (Break activity in work sequence as in the Method statement)	Hazard /Aspect Hazard is anything with potential to cause harm or loss.	HSE Risk Risk is the harm resulting from the hazard.	EXISTING CONTROL MEASURES	Rating (see enclosed legend page for details) OHS & E S L	Risk Value R = S x L OHS S x L
				brought to site. • Workers to be trained in safe use of COSHH material.	4 5 L	20 OHS S x L
				outside the building. • Spill kit to be available in the storage area.	3 L	3 OHS & E S x L
8	Diesel storage	Storage in an inappropriate tank, no bund wall, handling by unauthorised person	Fire loss of life Property damage Env. damage	• Diesel storage should be approved tanks only. • Bund wall and drip tray to be provided. • Appropriate fire extinguisher shall be placed nearby. • Spill kit to be kept nearby.	4 5 L	20 OHS S x L
				Care shall be taken to avoid spillage while decanting. • It should be filled by only plant div. diesel tanker. • Approved nozzle to be used. • Sign boards- "flammable material" and "No smoking" should be placed.	3 1 L	3 OHS & E S x L

* Date: 1712/2025
